
Response to

RFP LLA : Sales Digital Transformation – Rationalization + MACD

March 2026

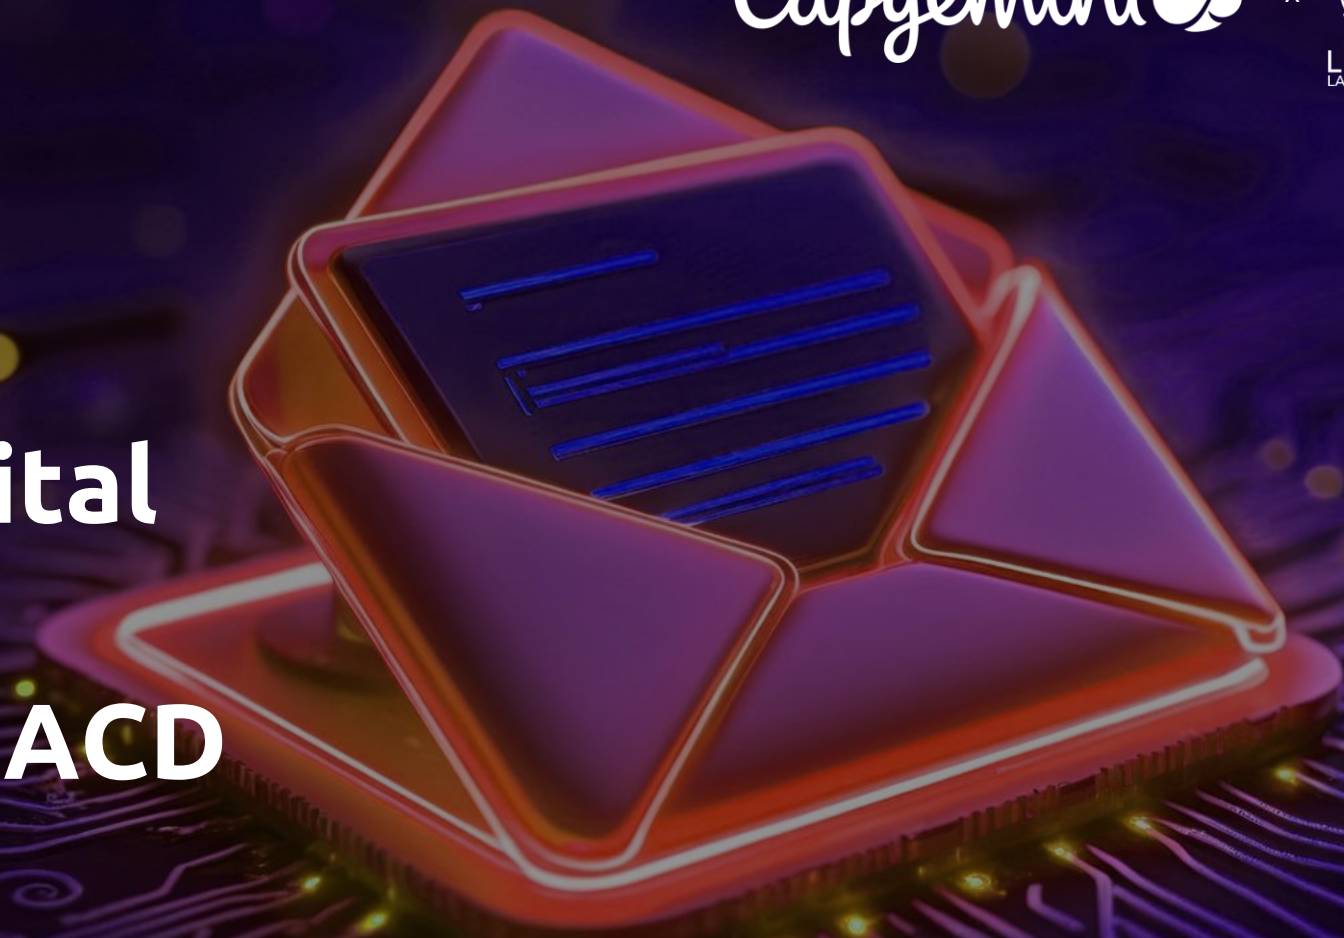

Make it real.

Agenda

1. Executive Summary
2. Why Capgemini?
3. Scope, Strategy, Definition & Design Principles
4. Phase 1 Solution
5. Phase 2 Solution
6. Assumptions, Dependencies, Risks & Out of Scope
7. Delivery Plan & Governance Model
8. Commercials
9. Optional Production Support Model
10. Future Roadmap

Company Confidential © Capgemini 2026. All rights reserved.

Executive Summary

Executive Summary



Thank you for providing Capgemini with the opportunity to participate in the Sales Digital Transformation Rationalization + MACD Solution for the Caribbean. We understand the importance of the success of this initiative and are committed to delivering a scalable, modernized, and insight-driven Enterprise Sales ecosystem that aligns fully with Liberty Caribbean B2B's strategic vision.

To ensure measurable value and business readiness, the transformation will be executed in two phases.

- Phase I lays the foundation through product catalog design & configuration, enhanced sales flows, improved governance, and UI upgrades.
- Phase II expands into full MACD automation, comprehensive asset lifecycle management and high-performance bulk processing capabilities. Together, these phases create a unified, future-ready platform capable of supporting current needs while seamlessly scaling across markets.

Being incumbent – Capgemini is not just ***uniquely positioned to help LLA deliver this successfully but also for future extension and expansion***

- We understand **B2B SF landscape** well
- We are incumbent service provider for **integration as well testing services ,** hence bringing best benefits of reusability, cross leverage and also most well positioned to deliver an end-to-end service
- Given the long-term partnership, we are willing and flexible to work on engagement model and delivery approaches best aligned to LLA B2B vision and roadmap




At Capgemini, we pride ourselves on a collaborative, "One Team" approach that integrates with LLA's existing processes, teams, and culture. By building trusted working relationships and driving toward a common mission, we bring the partnership mindset required to ensure the success of the Sales Digital Transformation Rationalization + MACD program

Company Confidential © Capgemini 2026. All rights reserved.

Why Capgemini

Capgemini Delivers A Cost-Efficient, AI-Driven and Scalable Solution for LLA

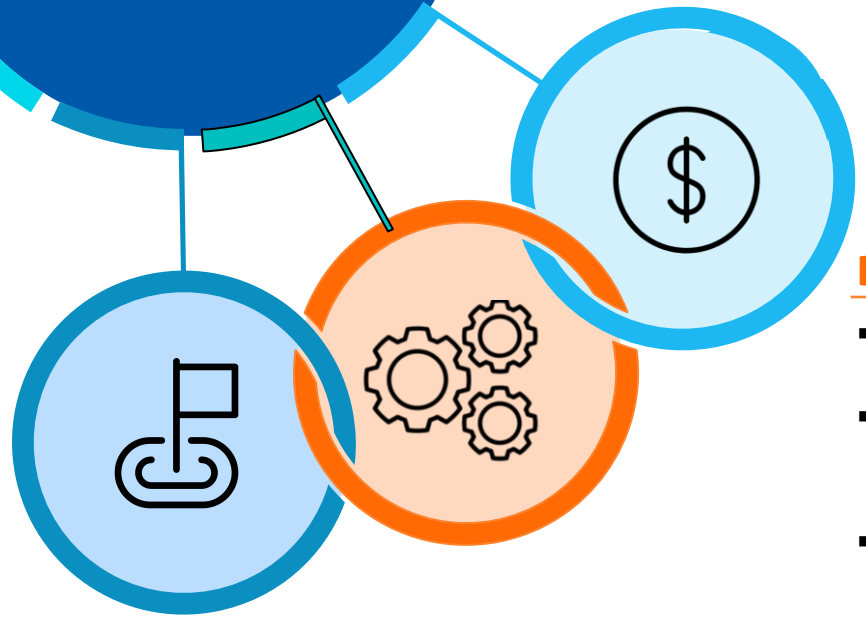

FUTURE-READY & COST-EFFICIENT SOLUTION

- Standardized Implementation Processes Across Markets Using LATAM Work Order Automation delivered by Capgemini team.
- **Proven C360 & data model expertise** for efficient business operations.
- Maximize **ROI** capitalizing on GenAI based productivity.

DIFFERENTIATORS

- **Leveraging frameworks like Amplifier for AI-Powered GenAI Testing** ~15% effort reduction in test design.
- Capgemini brings deep, hands-on understanding of **end-to-end Enterprise sales journeys** in **LATAM & Caribbean markets**. This enables the programme to move **directly into execution** without extended discovery or relearning cycles.
- A new supplier would need significant time to understand **existing sales processes, historical product structures, MACD nuances, asset models and billing integrations**.

THE CAPGEMINI ADVANTAGE

- Faster go-live with market agnostic solution**.**
- Scalable, AI-enabled, and **future-proofed** solution.
- **Proven telecom & Salesforce expertise** for LLA's success.
- 5+ years of proven expertise in SF and SFI development, system integration, and comprehensive testing, with deep exposure to the LLA technology landscape.
- A **deep understanding of the LLA product catalog**, including **product structures**, **cross-market variations**, and the associated complexities in **product configuration and decomposition.**
- Proficient in navigating US DOJ and DOD compliance expectations and implementing all required procedures for Puerto Rico and USVI markets

Company Confidential © Capgemini 2026. All rights reserved.

Business Value of SF Sales Digital Transformation

- Integrated E2E Sales and provisioning (Work Order Automation) in LATAM reduces time-to-install and manual effort. This can be enriched as future roadmap with Billing Integration for E2E automation
- Work Order Automation offers a cost-effective and flexible solution for LATAM legacy flows and extendable to CWC
- High flexibility for customization to meet complex business rules across diverse markets
- Scalable architecture supporting Legacy Product Catalogues
- Compatible with existing “CSC support” processes
- Reduction in training cost for Business Users on Sales and Care flows

Company Confidential © Capgemini 2026. All rights reserved.

Scope, Strategy, Definition & Design Principles

Make it real.

Capgemini x LIBERTY LATIN AMERICA

Functional Scope

The scope of work is to modernize the Enterprise Sales journey across the complete service lifecycle in the Caribbean market, leveraging the Salesforce CRM platform as the foundation. This programme will be executed in two phases:

Phase I – Foundational Modernization

- Phase I focuses on establishing the core building blocks required for a streamlined and scalable sales ecosystem, including:
  - Product catalog configuration
  - Enhanced sales flows for improved efficiency and reduced manual effort
  - Strengthened governance across the sales process
  - User interface (UI) upgrades to deliver a consistent and intuitive experience
  - Bulk New Connect



Phase II – Advanced Automation & Operational Excellence

- Phase II extends the capabilities introduced in Phase I by enabling:
  - Full MACD automation (Move, Add, Change, Disconnect) and Comprehensive asset lifecycle management
  - High-performance bulk processing to support large enterprise transactions




Together, these two phases deliver a future-ready, scalable, and unified sales platform that enhances operational efficiency, supports complex enterprise workflows, and adapts seamlessly across markets in the Caribbean region.
2 Options are proposed as part of overall solution in Phase-I and Phase-II –

Option A: Without any integration. **Option B**: With Billing Integration for Provisioning only

Company Confidential © Capgemini 2026. All rights reserved.

Phase 1 Use Cases


Phase I – Product Configuration & Sales Journey Foundation

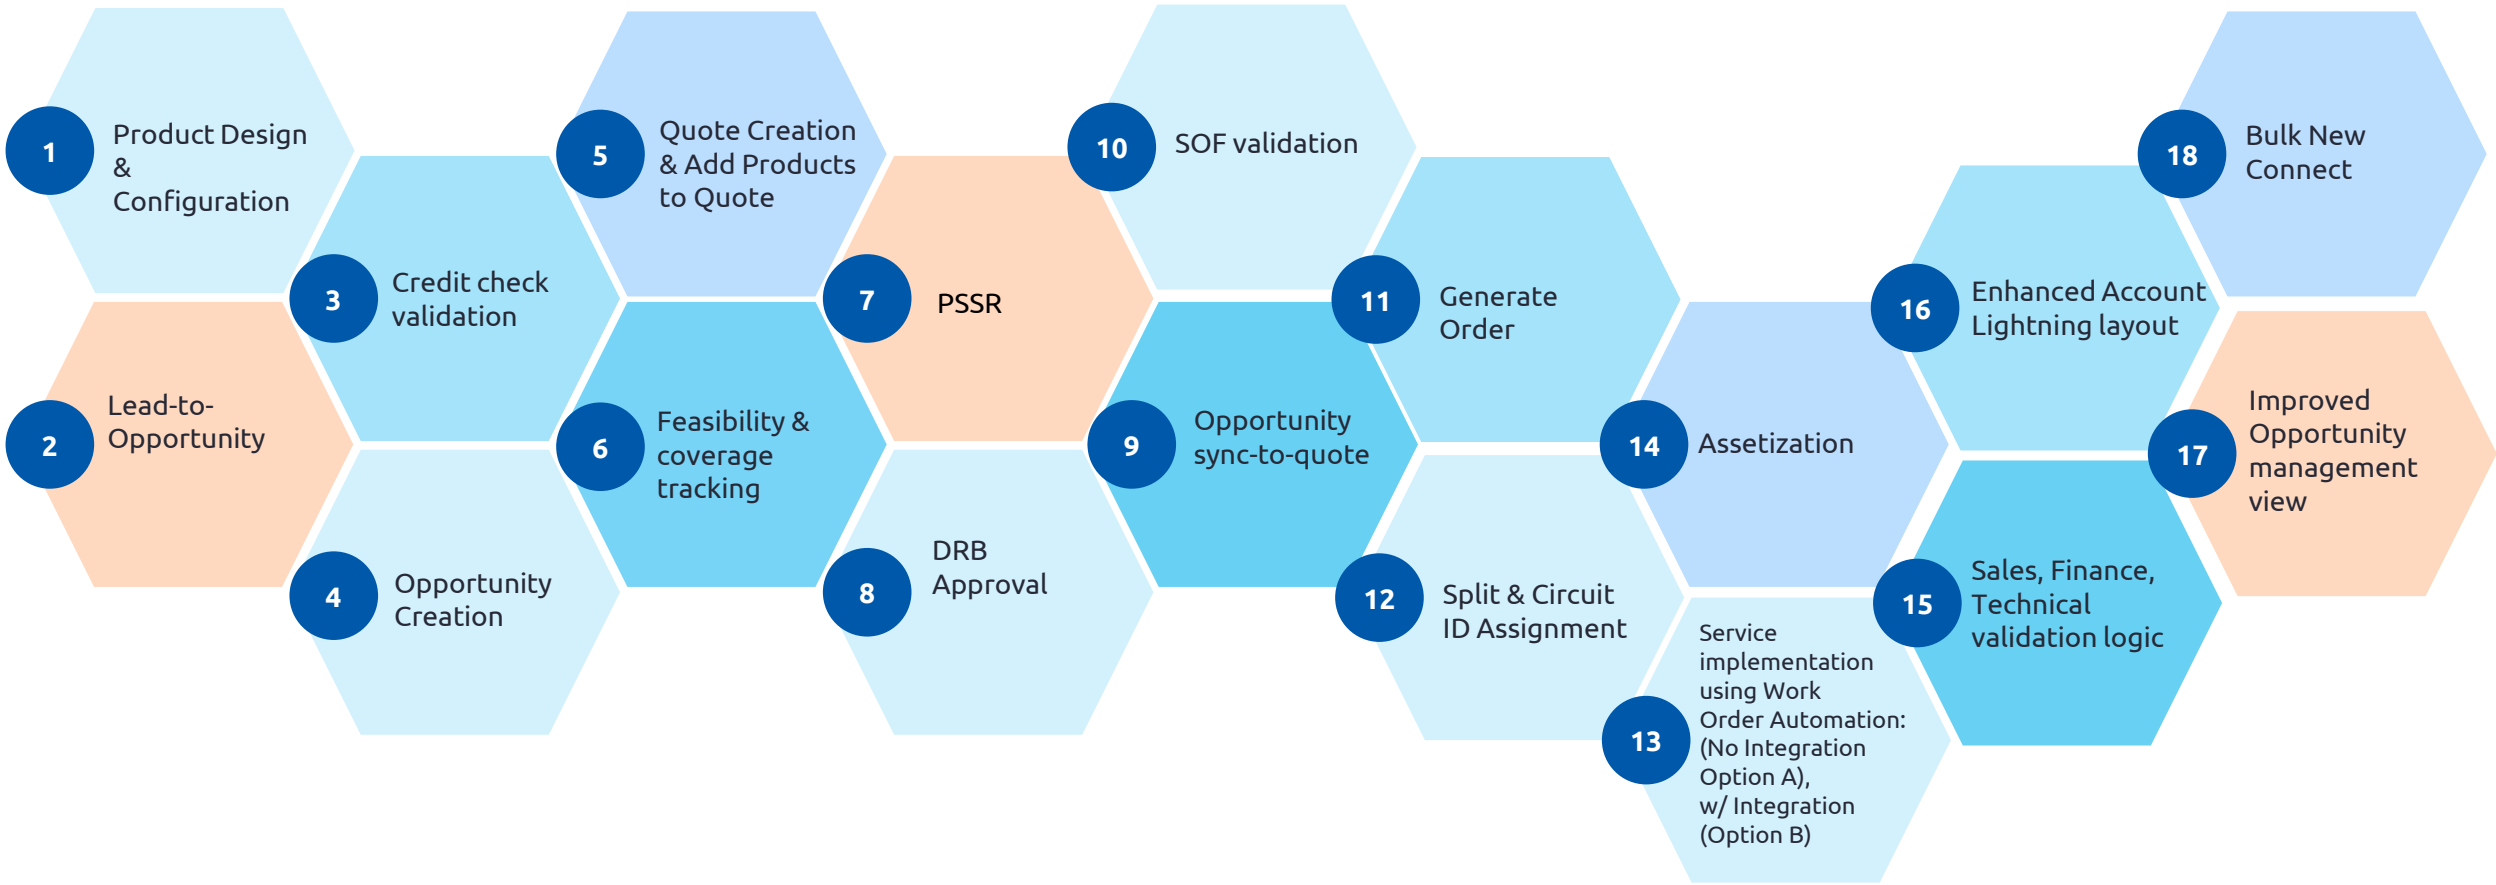

Company Confidential © Capgemini 2026. All rights reserved.

Phase 2 Use Cases


Phase II – MACD & Lifecycle Transformation

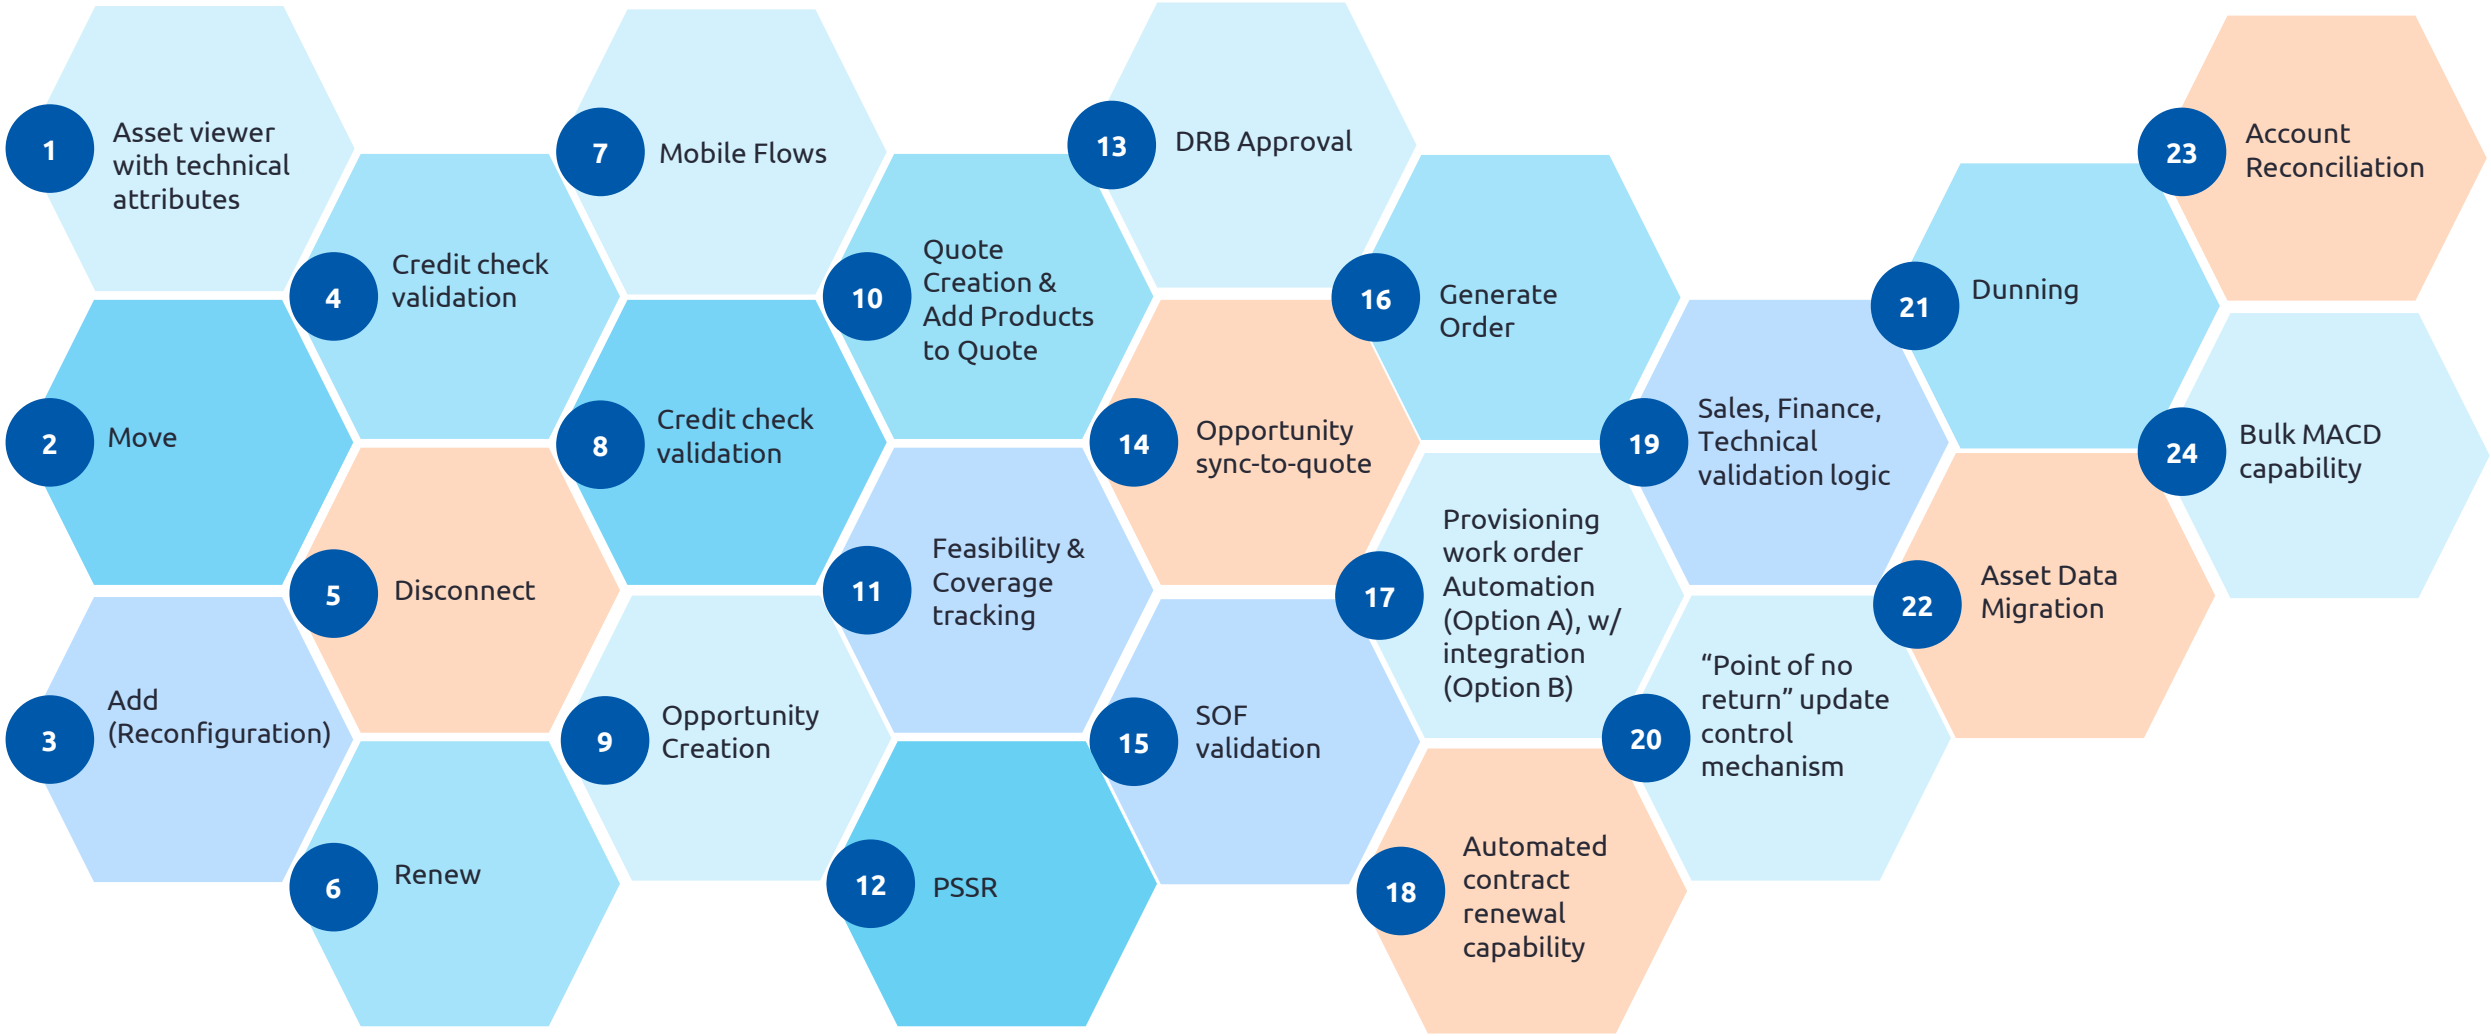

Company Confidential © Capgemini 2026. All rights reserved.

Product families in Scope

The mentioned 7 product families are in scope, with an expected volume of up to 200 products.

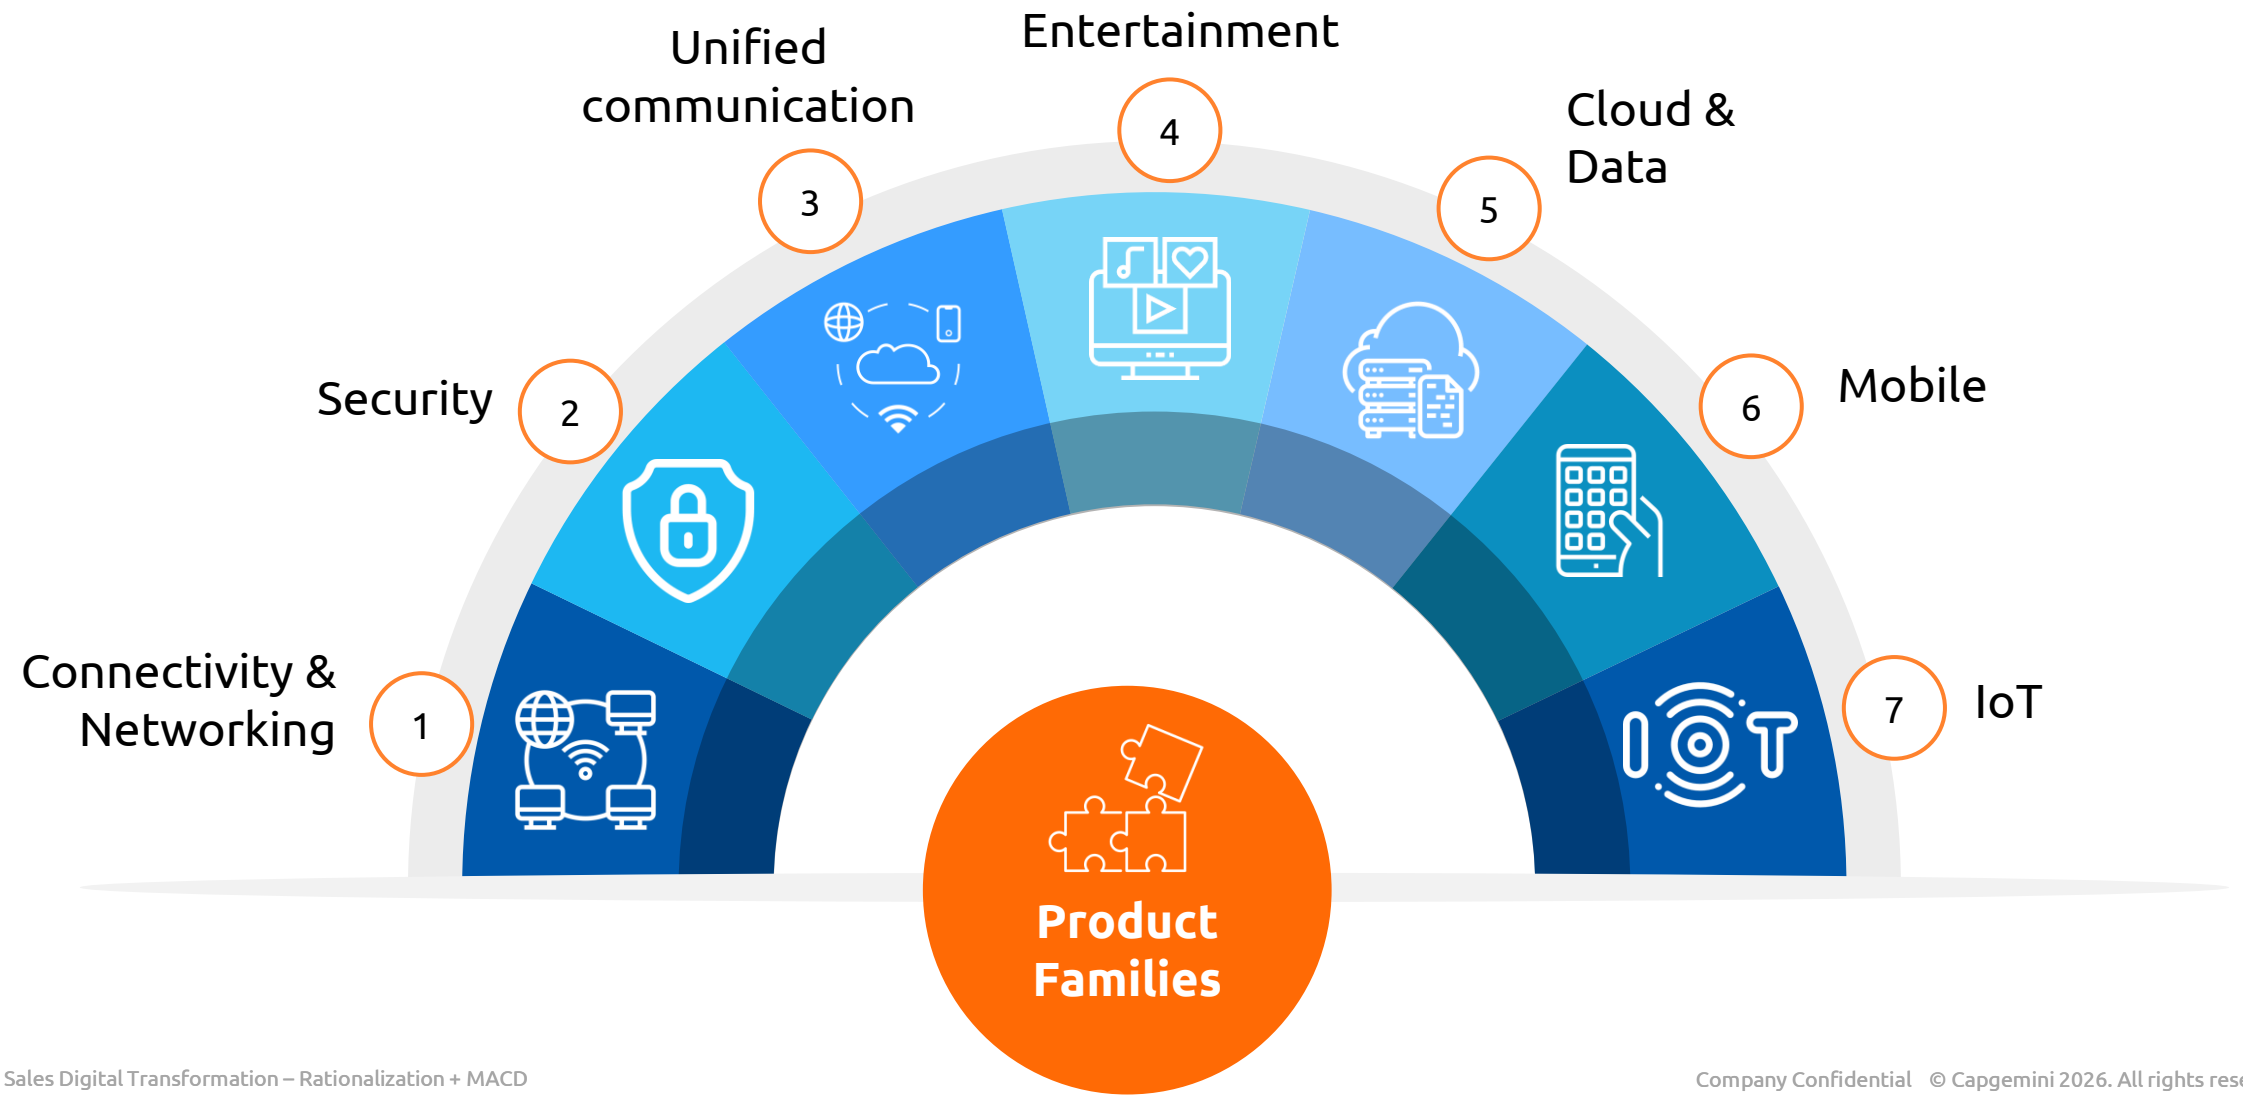

Company Confidential © Capgemini 2026. All rights reserved.

Non-Functional Requirements



Performance

- MACD flow completion in less than 5 mins up to 100 assets
- Bulk operations for both MACD and New connect scalable to 1000 assets
- Solution must support ~100 concurrent asset operations


Reliability

- Go-live threshold: ≤5% open high-priority bugs in UAT

Company Confidential © Capgemini 2026. All rights reserved.

Execution & Rollout Strategy

- The implementation will be delivered on Salesforce Lightning, as it is recommended for an enhanced and modern UI experience.
- As part of product configuration, the project will leverage the existing Pricing Automation framework and data model, with only essential adjustments required to support the redesigned process.
- The proposed solution will be market-agnostic, enabling a standardized sales process across all Caribbean markets. Any market-specific variations will be recommended for alignment through business process adjustments, rather than system customization.

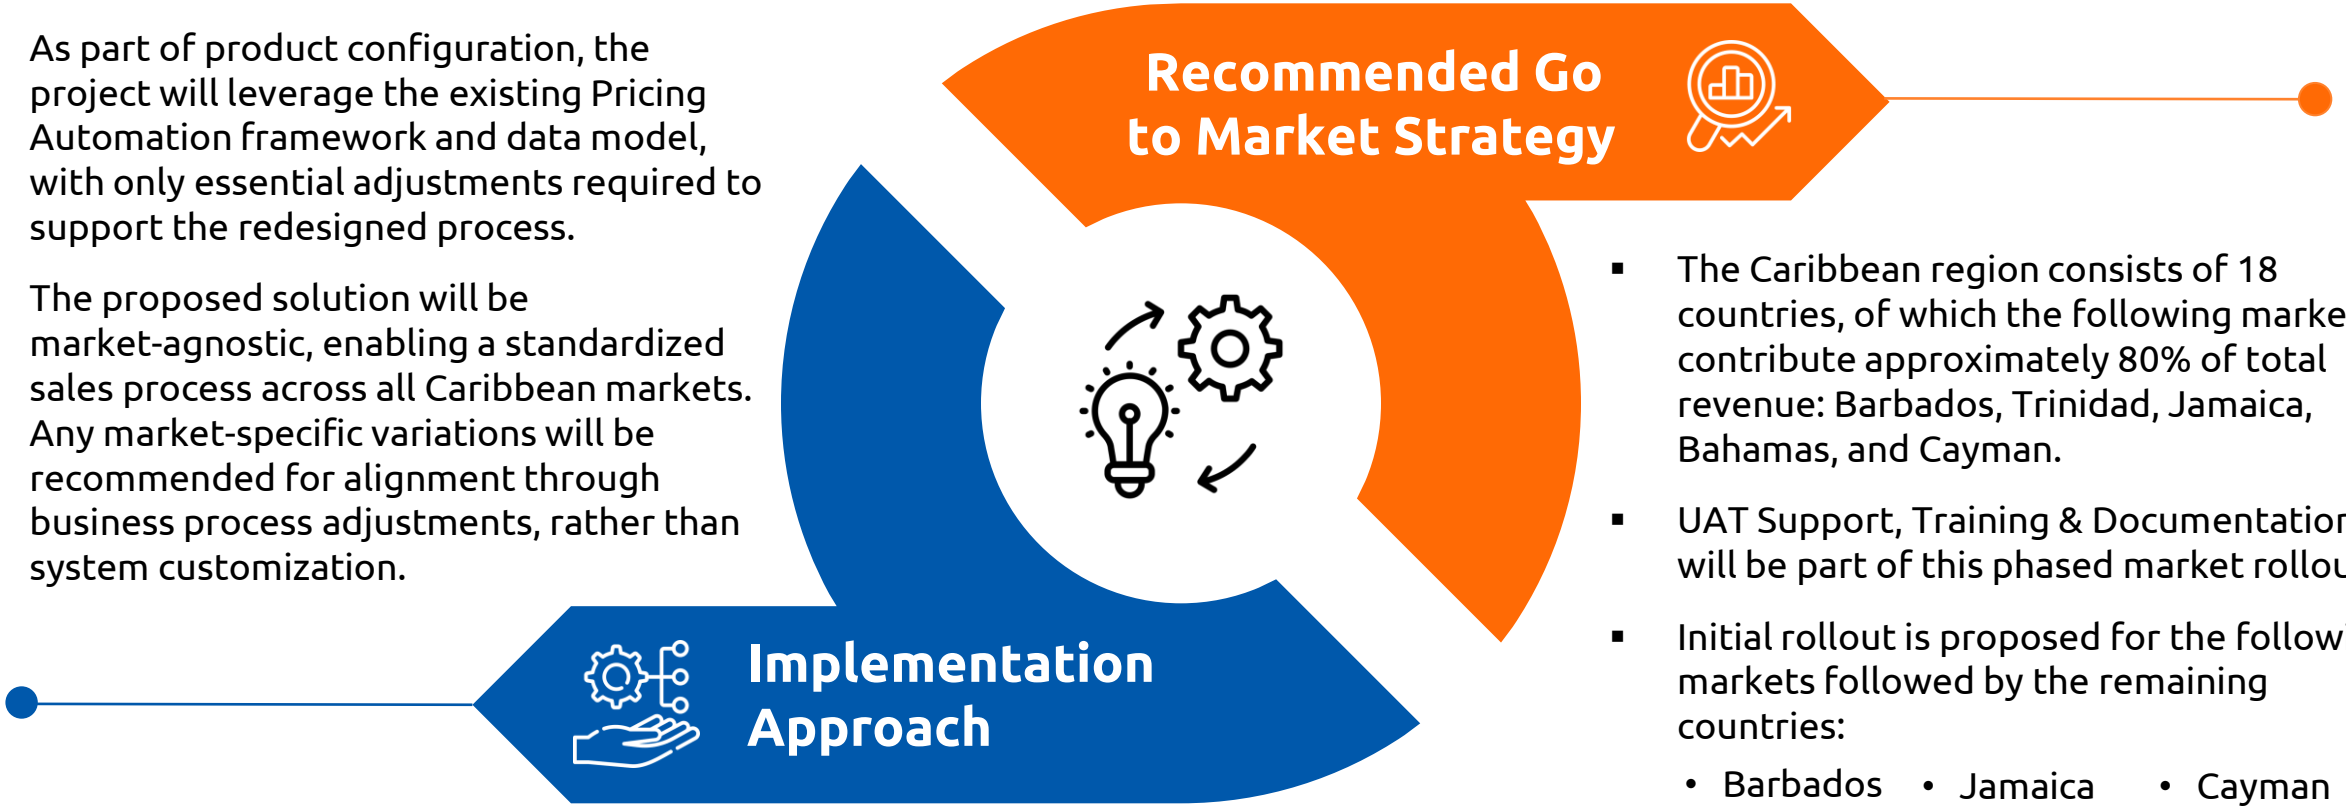

- The Caribbean region consists of 18 countries, of which the following markets contribute approximately 80% of total revenue: Barbados, Trinidad, Jamaica, Bahamas, and Cayman.
- UAT Support, Training & Documentation will be part of this phased market rollout.
- Initial rollout is proposed for the following markets followed by the remaining countries:
  - Barbados
  - Trinidad
  - Jamaica
  - Bahamas
  - Cayman

Company Confidential © Capgemini 2026. All rights reserved.

Profiles Definition and Configuration

The Caribbean sales journey would be used by following main personas, around which the profile configuration can be implemented –



Sales Team (Agents and Manager)

Responsible for selling products



Implementation Team (Service Implementation Associates and Managers)

Responsible for installation of services and other related technical work




PMO

Responsible to oversee implementation process execution by Service Implementation Teams

Company Confidential © Capgemini 2026. All rights reserved.

Key Design Principles

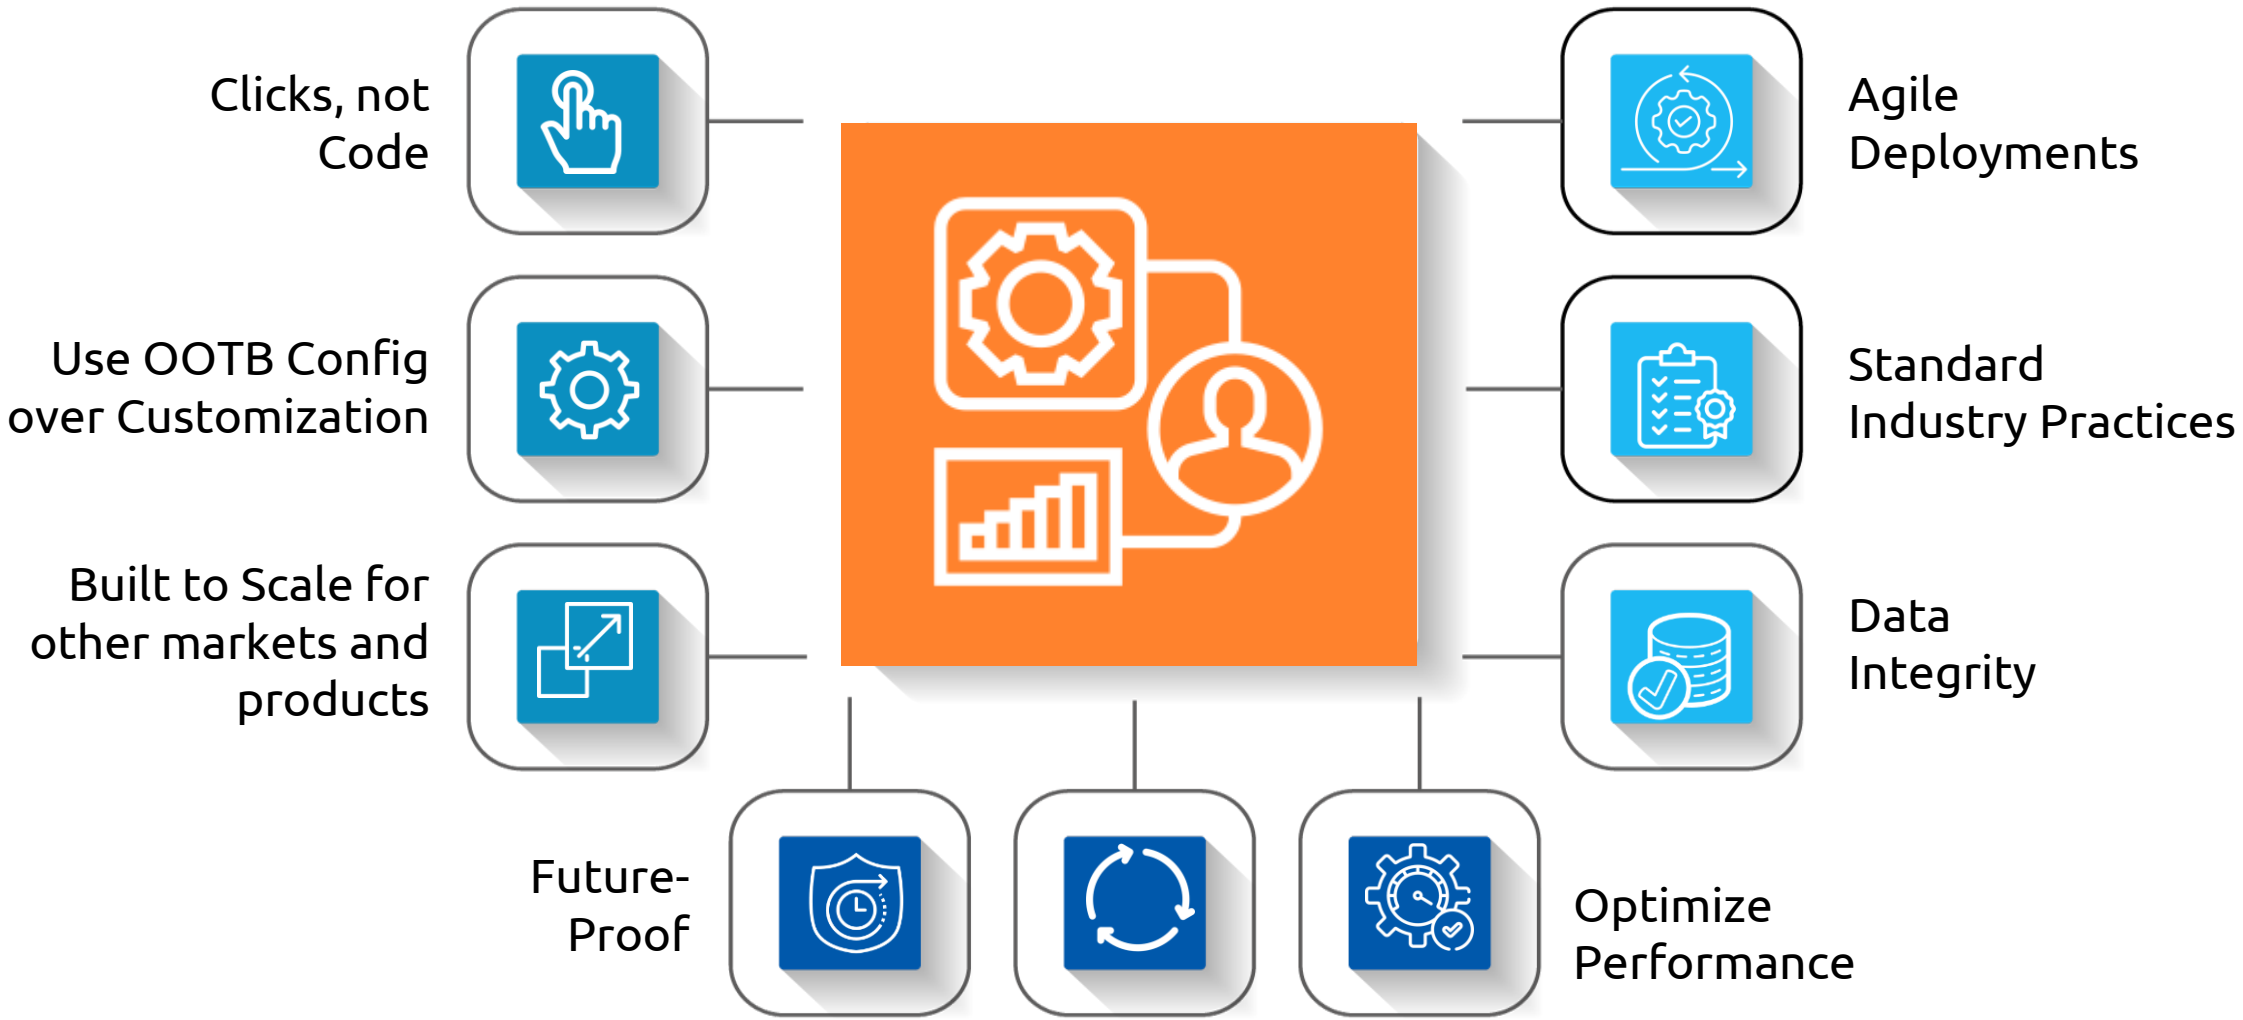

Company Confidential © Capgemini 2026. All rights reserved.

Phase 1 Solution

Make it real.

Capgemini x LIBERTY LATIN AMERICA

Proposed Phase-I Solution (1/6)

This phase will include Product Configuration and New Service Sales Journey for Existing and New Customers.



Proposed Sales Journey for Enterprise Caribbean Markets will be implemented based on Pricing Automation Process framework used in LATAM.




For New Customers, the journey would start from Lead Conversion (Standard Salesforce Process) to create Account, Contact and Opportunity and so on.



While for Existing Customers, it would start from Opportunity Creation from Account View.


Proposed Sales Flow (New Customer) – Lead Conversion

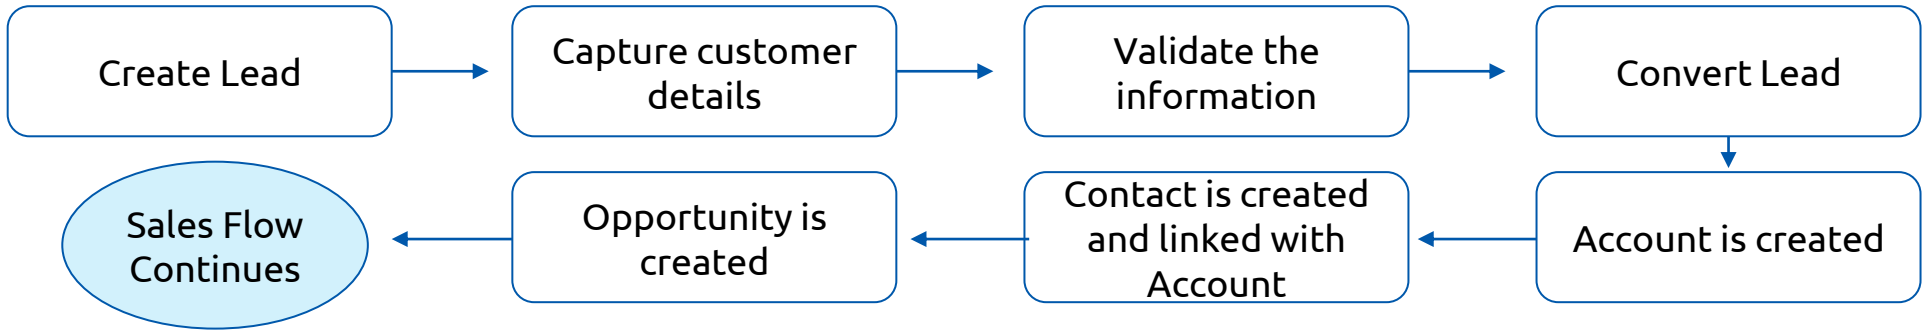

Company Confidential © Capgemini 2026. All rights reserved.

Proposed Phase-I Solution (2/6)


Proposed Sales Flow (Exiting Customer)

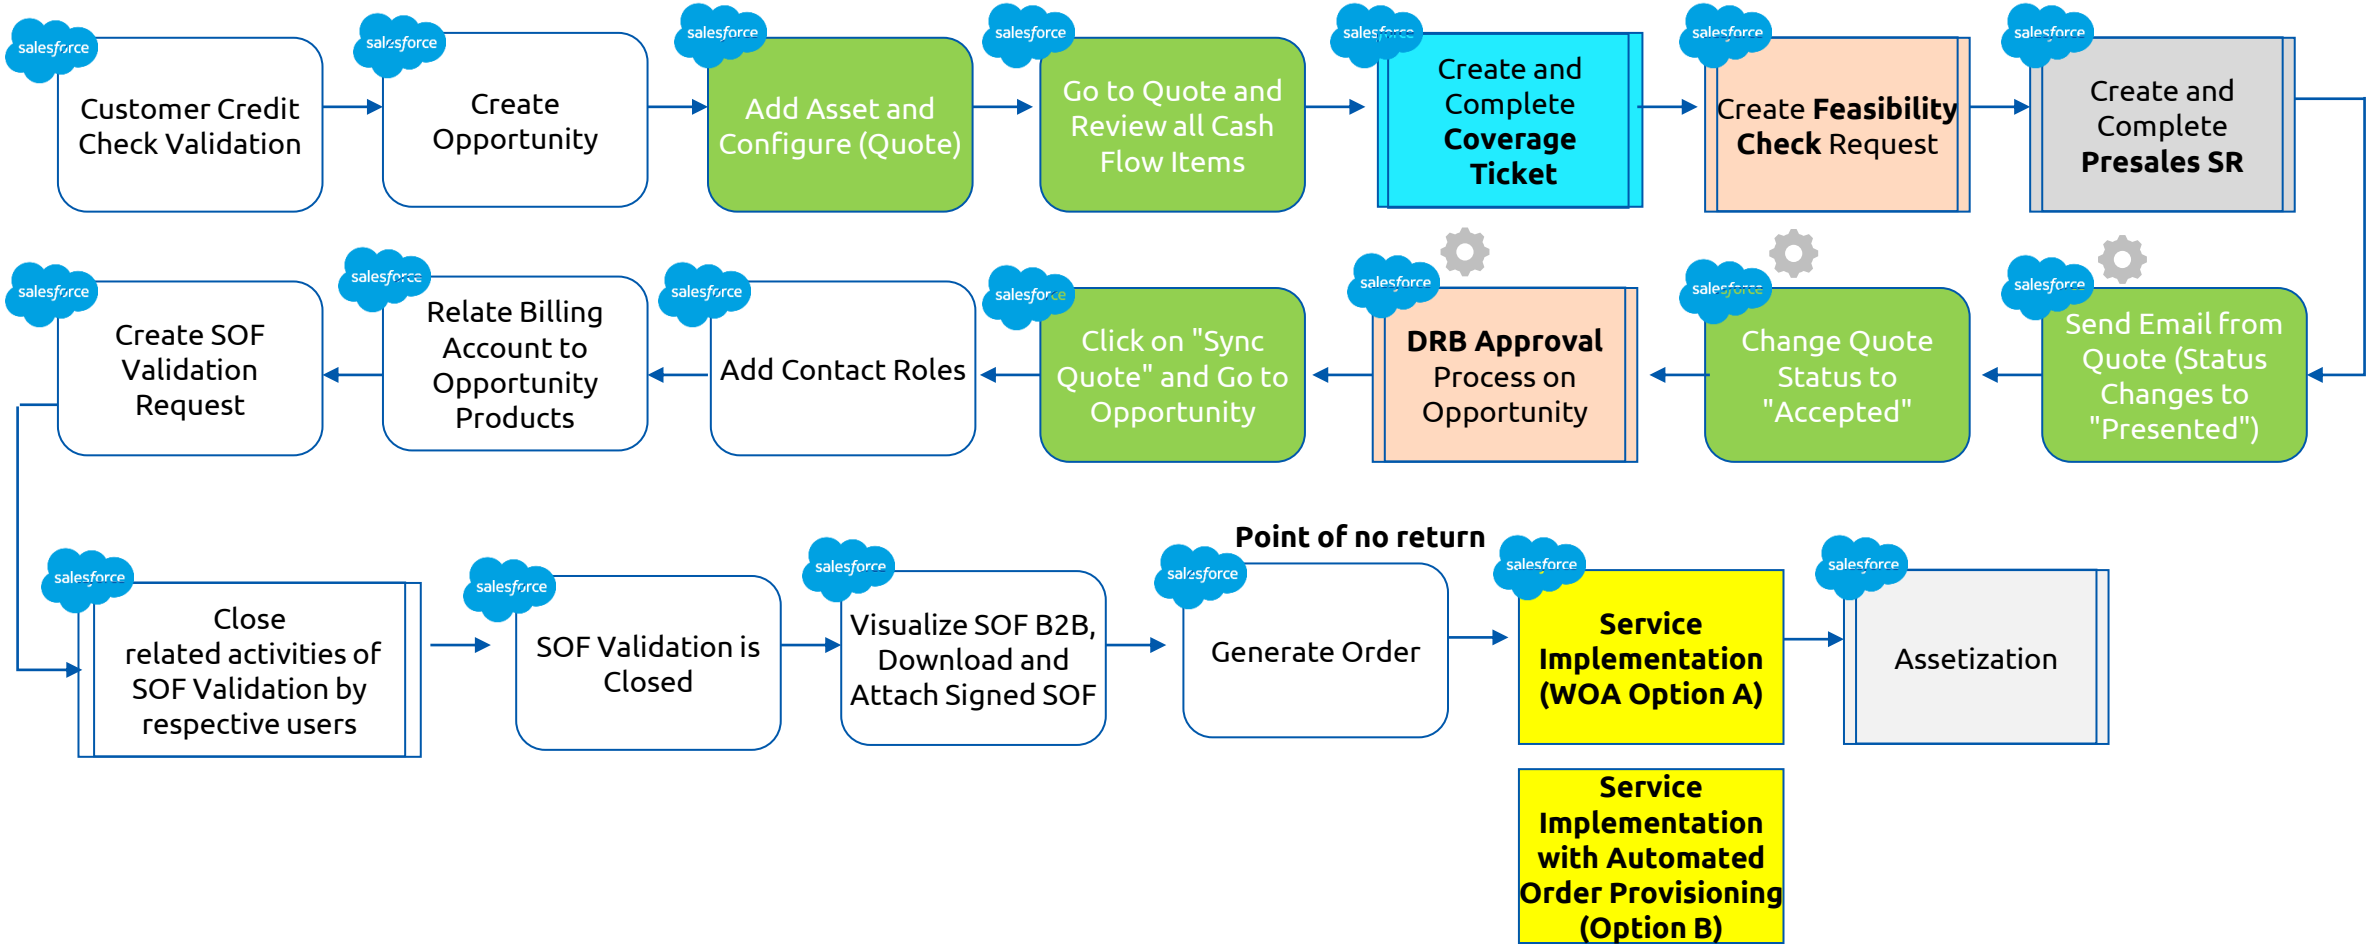


Company Confidential © Capgemini 2026. All rights reserved.

Proposed Phase-I Solution (3/6)


Coverage Ticket



Feasibility Check




Presales SR




Company Confidential © Capgemini 2026. All rights reserved.

Proposed Phase-I Solution (4/6)

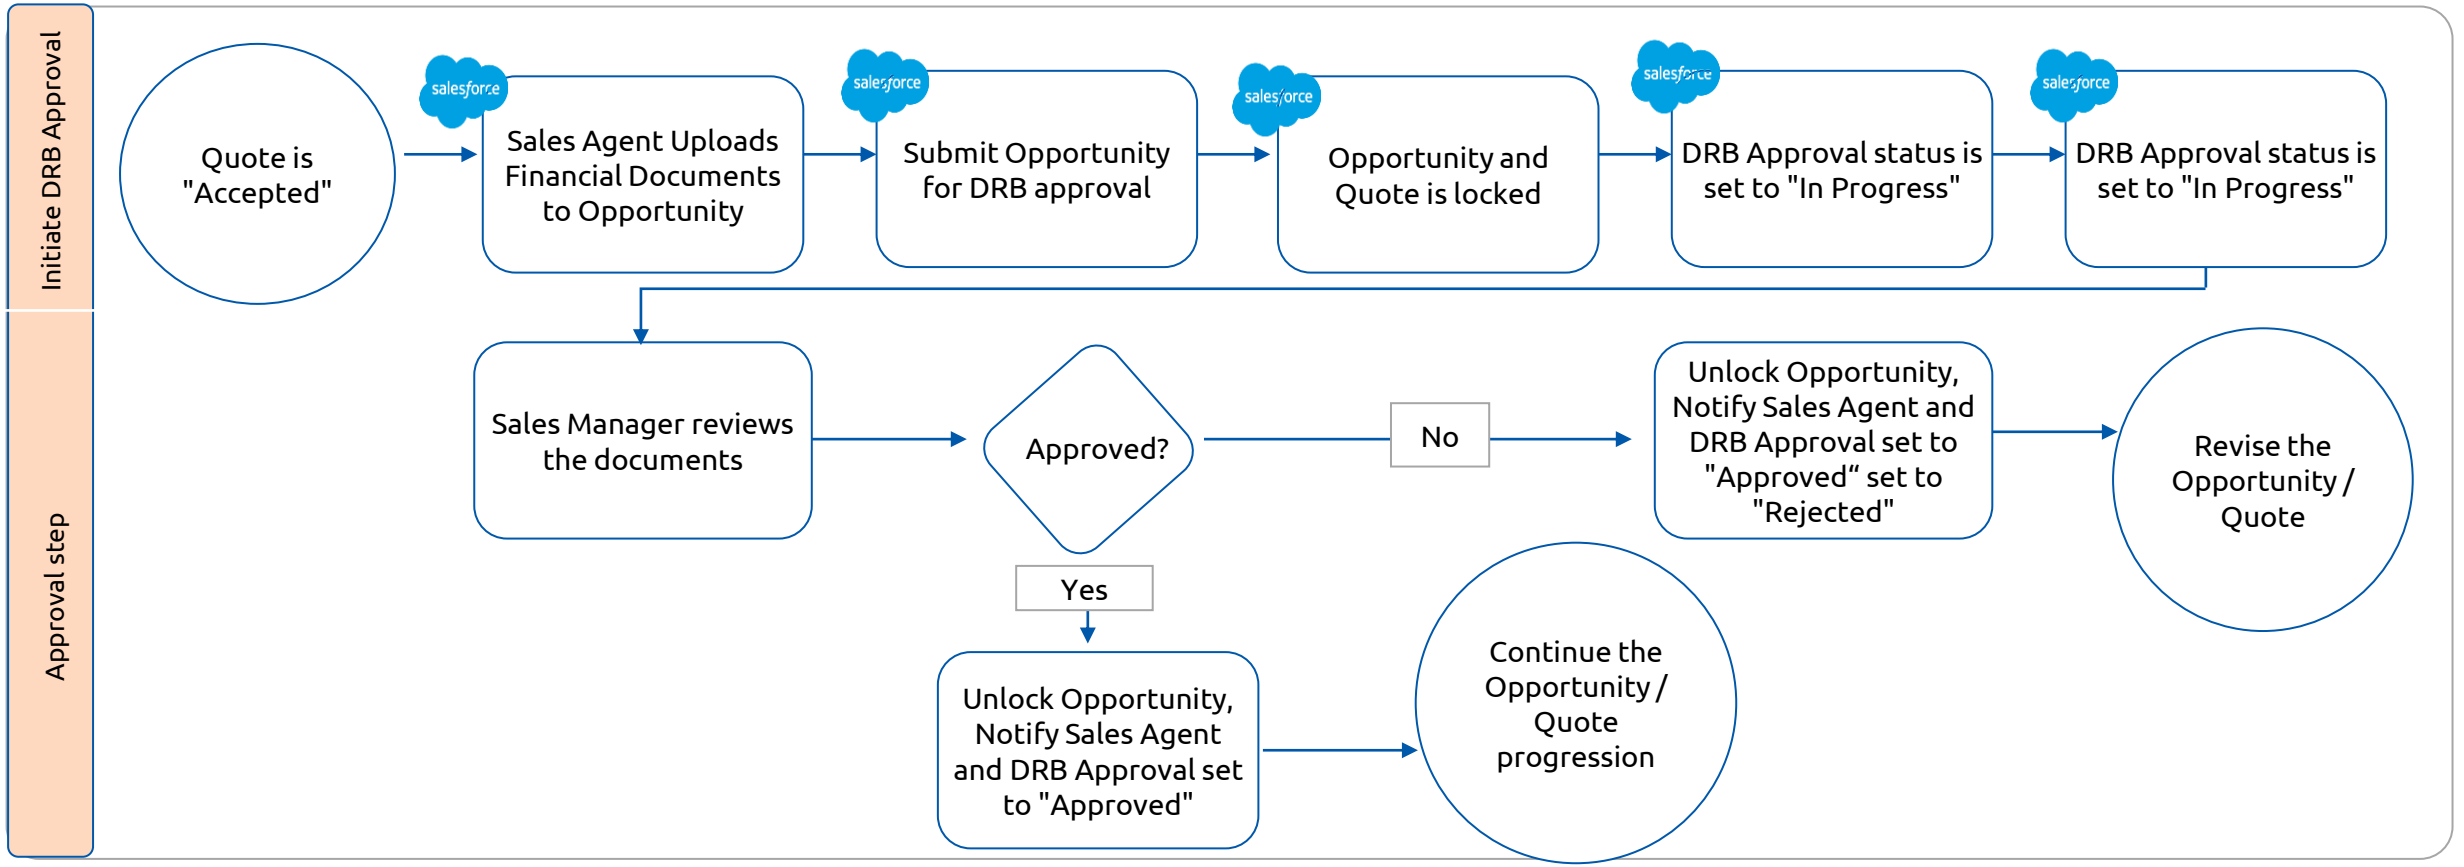

Service Implementation




Company Confidential © Capgemini 2026. All rights reserved.

Proposed Phase-I Solution (5/6)

Bulk New Connect Process:

- Once New Connect scenarios are in place for Sales journey, a Bulk feature will be introduced to process multiple (>1000 Line Items) line items for New Connect process.
- Following diagram explains high level process flow for Bulk New Connect process -

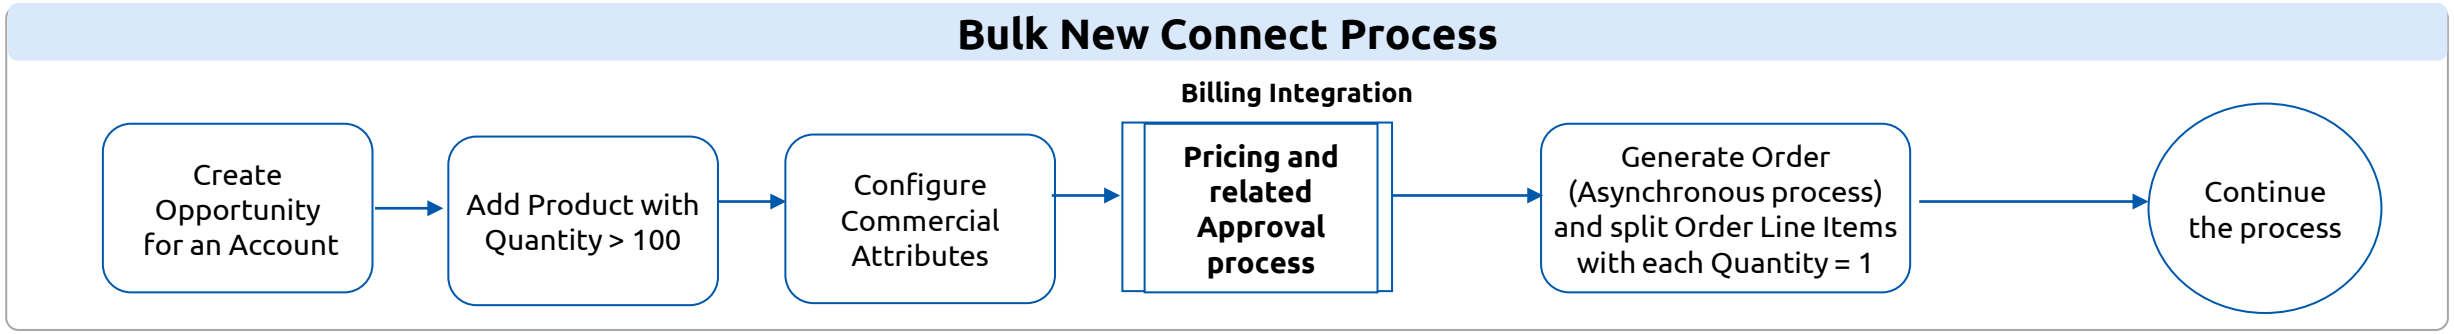

Company Confidential © Capgemini 2026. All rights reserved.

Proposed Phase-I Solution (6/6)

UI Enhancements for Account, Asset and Opportunity Management



Enhanced Account Lightning layout:

Proposal is to leverage existing C360 Layout to adopt Caribbean Account Data Model.

- The new Enhanced Account UI will include only the following features -
  - Account details
  - Related Contacts
  - Related Billing Accounts available in Salesforce (No Integrations)
  - Locations
  - Related Salesforce Cases



Improved Opportunity management view : Making sure to incorporate additional details to the existing view of Opportunity to track the type of transaction the opportunity is related to (upgrade, downgrade, disconnection, new service).

Company Confidential © Capgemini 2026. All rights reserved.


Capgemini x LIBERTY LATIN AMERICA


Phase 2 Solution

Make it real.

Proposed Phase II – Solution (1/5)

MACD & Lifecycle Transformation(MACD)
High Level Process Flow for MACD Service Sales Journey based on existing LATAM Pricing Automation Flow –

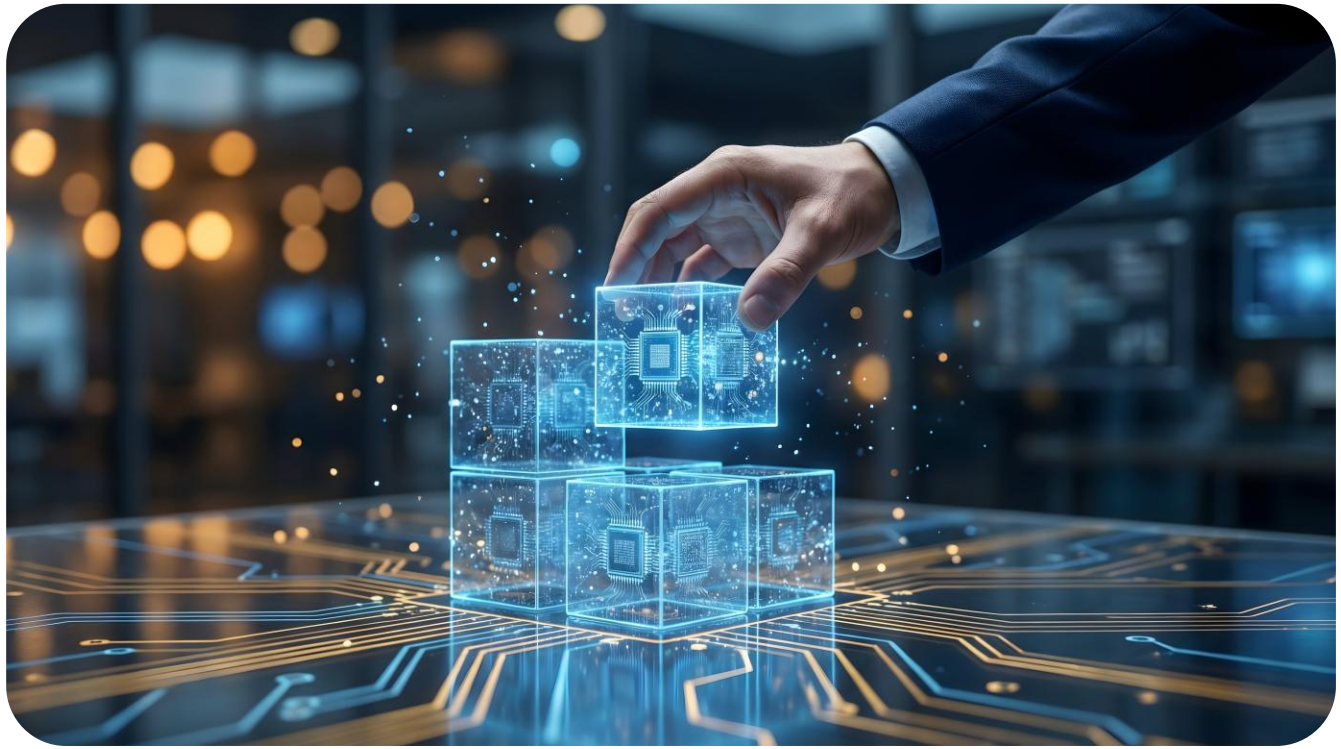

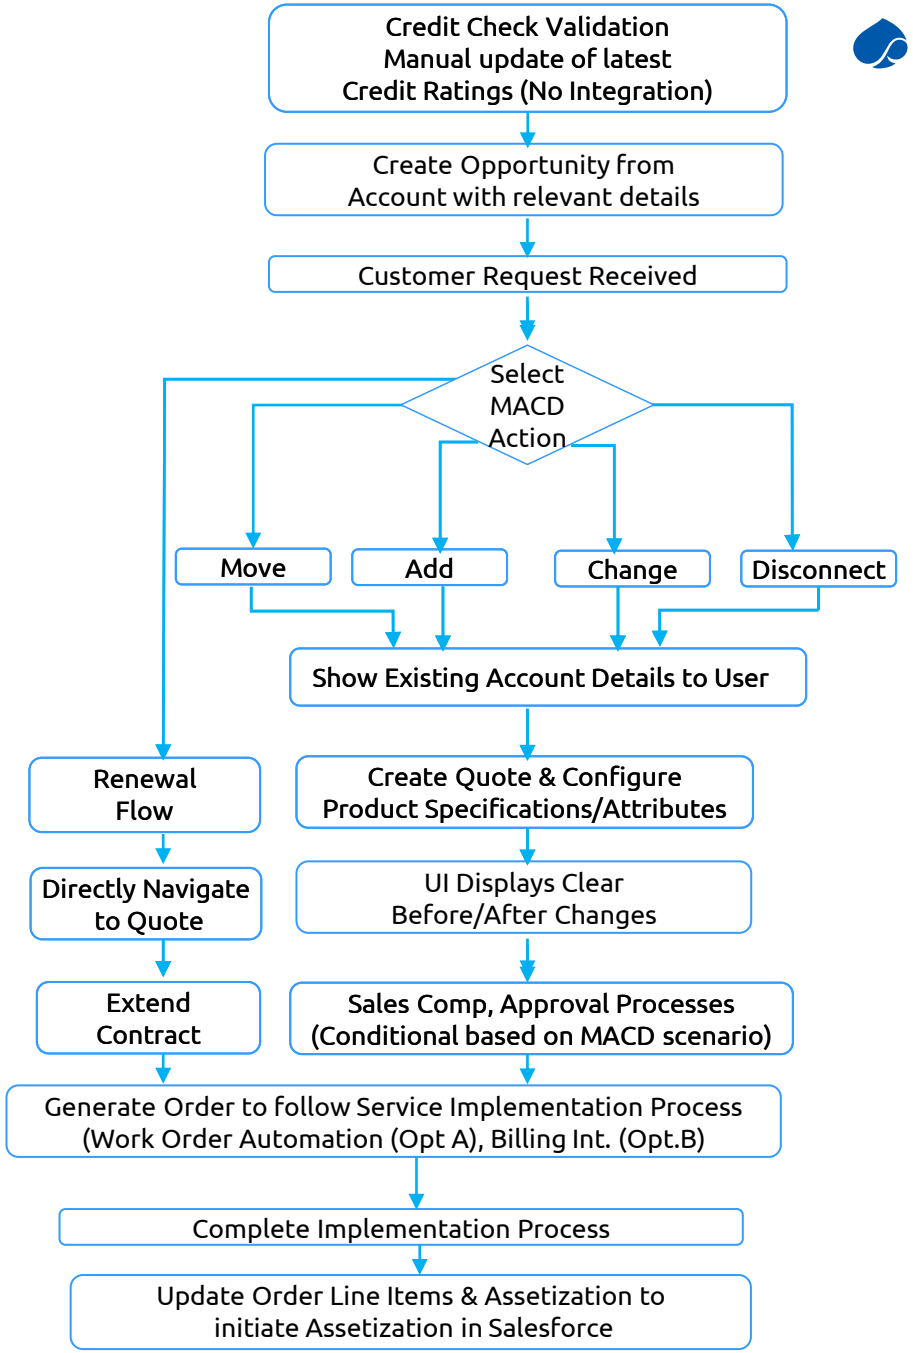


Company Confidential © Capgemini 2026. All rights reserved.

Proposed Phase II – Solution (2/5)

Bulk MACD Process:

- Once all MACD scenarios are in place for Sales journey, a Bulk feature will be introduced to process multiple assets for MACD transactions.
- Following diagram explains high level process flow for Bulk MACD process -

Bulk MACD Process




Company Confidential © Capgemini 2026. All rights reserved.

Proposed Phase-II – Solution (3/5)

Account Migration strategy


- Account Data Migration includes Data clean up and correction in existing account in salesforce.
- That would comprise of sync up between Billing system and Salesforce.

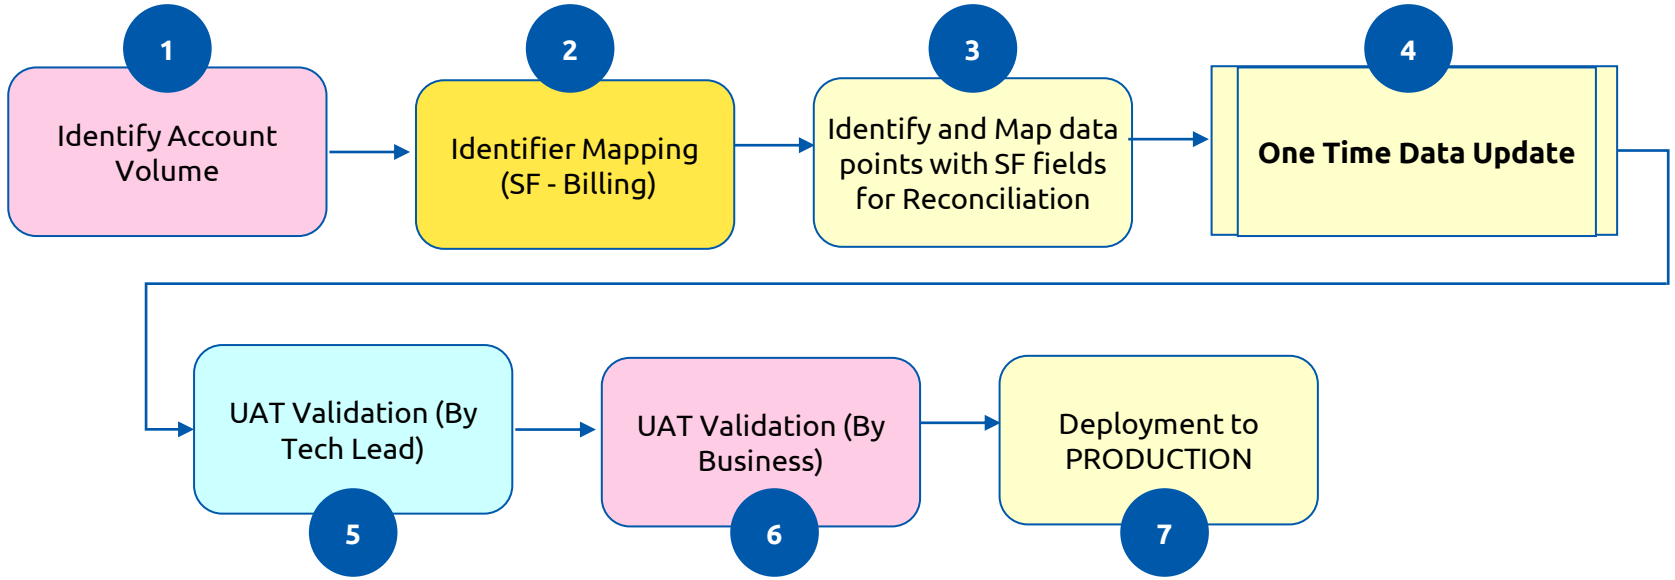

Company Confidential © Capgemini 2026. All rights reserved.

Proposed Phase-II Solution (4/5)

Asset Migration Strategy

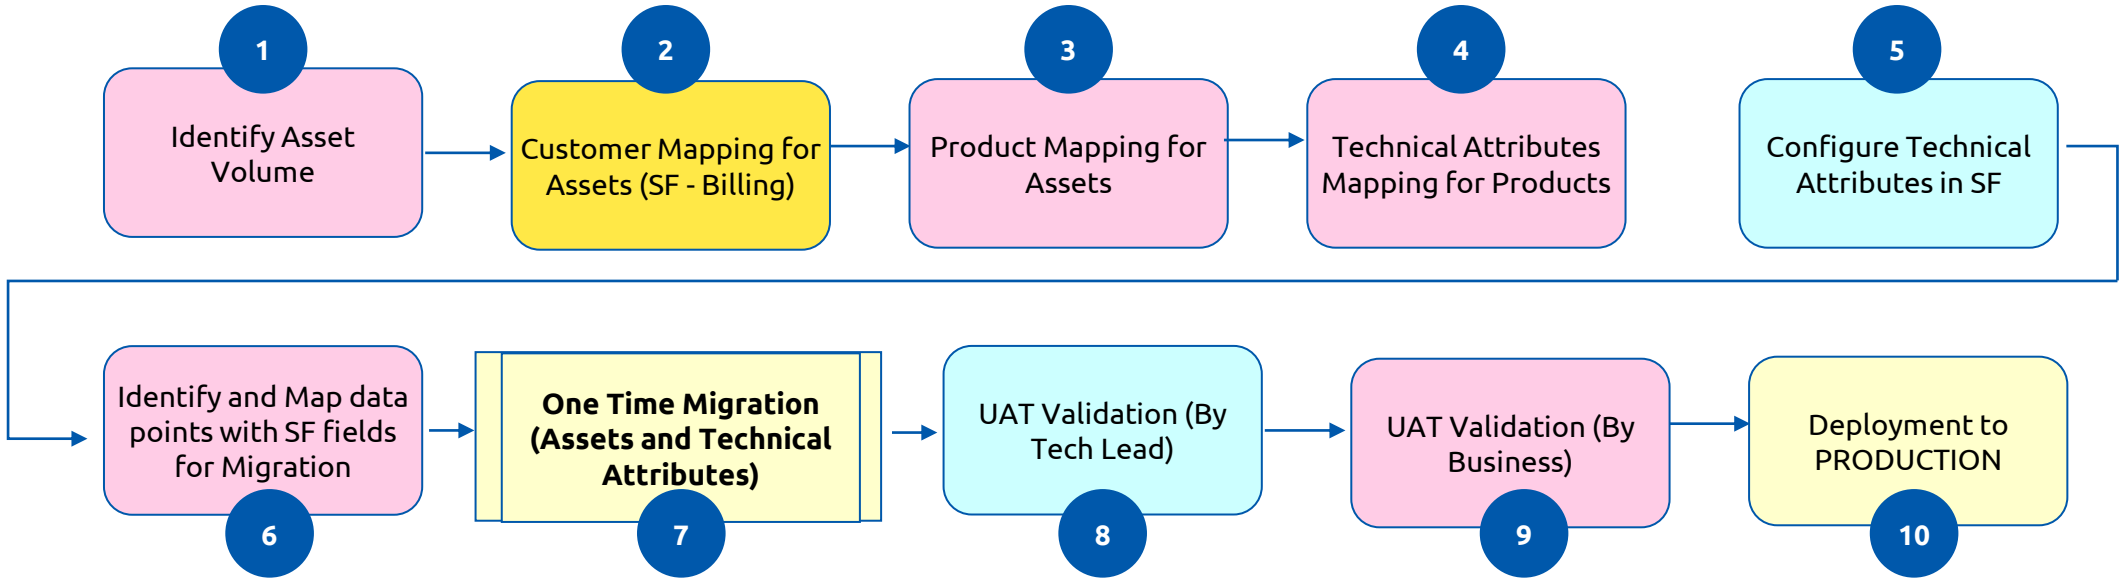

Legends

- Owner - Business
- Data Migration Team
- Development Team
- Business & Data Migration Team

Company Confidential © Capgemini 2026. All rights reserved.

Proposed Phase-II Solution (5/5)

Data Migration Considerations



- Data quality thresholds (minimum):
  - Required fields completeness ≥ 98% (e.g., Asset Name, Account, Product).
  - Duplicate rate ≤ 1% by key (Serial/External Asset ID).
  - Invalid references (e.g., missing Account/Product) ≤ 0.5%.
  - If thresholds aren't met, effort/schedule is re-baselined via change control.
  - All Account/Contact pricebook/ pricebook entries are existing with accurate data.
- Liberate, Cerillion and Amdocs are part of the current scope.
- Extraction of the raw data from all billing system must be provided with business alignment.
- Reference/master data is final (Accounts, Assets) and loaded/available in target prior to Asset loads.



Business availability

- SMEs (data owners) available ≤ 24h for clarifications during mapping/testing.



- On Demand Asset Migration will be assessed based on Request.

Company Confidential © Capgemini 2026. All rights reserved.

Gen AI Levers for Productivity Gains

- Capgemini Amplifier Gen AI Tool to be leveraged for –
  - Requirement Creation
  - Requirement Ambiguity Analysis
  - Requirement Refinement
  - Requirements to User Story Generation
  - Gherkin (Test scenarios)

- GitHub Copilot Tool to be leveraged for –
  - Code Generation with context
  - Test Class/Test Coverage for Apex classes
  - Code Documentation
  - Configurations (Flows, Fields, layouts etc.)

Highlights of using Gen AI

Productivity Benefits

- Amplifier –
  - Standardised Templates
  - Accelerated Requirement Turnaround
  - Accelerated Testcases Turnaround
  - Reduced Rework Through Early Ambiguity Detection

- GitHub Copilot –
  - Standardized Prompt Library
  - Inline Code suggestions
  - Multi-Language Support
  - Test Case Generation
  - Learning and Documentation

- Using these GenAI tools, we anticipate overall productivity savings of approximately 12–15%, which has already been factored into the total cost.
- The GenAI Amplifier is already deployed in the LLA cloud, though the number of users is currently capped. The setup supports up to 200 users; at present, 70 users are active, primarily for testing purposes. For any users beyond the 200-user limit, the cost is €100 per additional user.

Company Confidential © Capgemini 2026. All rights reserved.

Suggestive Agentforce Benefits

Automation of Scenario:
As part of this project, we are implementing following scenarios

1. Renewal
2. Suspend/Resume
3. Dunning

This can be automated for End User with **Agentforce Sales Agent** to get details from User and provide summary and recommendation to the user.

Highlights of using Agentforce

Business Benefits

- Quick and easy access.
- Recommendations on next possible actions
- Automation of the scenarios to help user to seek data and act on their behalf

- Agentforce implementation can be done in 2 phases –
  - Identify use cases and scope
  - Implementation
- Based on finalized scope and design of Sales Journeys, Agentforce use cases can be finalized.
- A separate plan and cost will need to be evaluated for these Agentforce use cases which can be taken up during the development phase.

Company Confidential © Capgemini 2026. All rights reserved.

Assumptions, Dependencies, Risks & Out of Scope

Make it real.

Capgemini x LIBERTY LATIN AMERICA

Assumptions

Sr No.	Key Delivery Assumptions	Applicable Phase
1	Updates to asset information, including technical parameters, monthly recurring revenue (MRR), and contract terms, are initiated within the BSS systems. However, these changes are not automatically synchronized with other dependent systems. As a result, agents must manually apply identical updates across multiple platforms (swivel chair approach).	Phase-1
2	LLA will be performing product rationalization. LLA to share the product list with Capgemini for final build. Expected volume: approx. 200 products across 7 below families: ▪ Connectivity & Networking ▪ Security ▪ Unified Communication ▪ Entertainment ▪ Cloud & Data ▪ Mobile ▪ IoT	Phase-1
3	The proposal includes effort for product design and configuration/build only. It does not include effort for product rationalization. If the client needs support for rationalization, it can be handled separately.	Phase-1
4	Products will be designed and built using the existing Pricing Automation Product Catalogue framework.	Phase-1
5	Only Salesforce catalogue will be configured and there will be no changes to Billing products.	Phase-1
6	For Unit Testing and QA Testing, 1–2 products per family will be used. Testing of all products will be done during UAT, led by client stakeholders.	Phase-1
7	Rollout will be prioritized for 5 countries: Barbados, Trinidad, Jamaica, Bahamas, Cayman as these are high revenue generating markets. Remaining market roll out (total 13) will be planned followed by this.	Phase-1
8	There will be one common sales flow for all Enterprise Caribbean markets. Any country-specific differences will be handled manually by agents.	Phase-1
9	The Salesforce application as the sales channel is only in Scope.	Phase-1
10	We will reuse the existing LATAM Pricing Automation sales process and tailor it for Caribbean need.	Phase-1

Company Confidential © Capgemini 2026. All rights reserved.

Assumptions

Sr No.	Key Delivery Assumptions	Applicable Phase
11	All pricing needs for in-scope products will be handled using the existing Pricing Automation engine.	Phase-1
12	Agents will do credit checks manually and capture the result in Salesforce Account. No credit check integration.	Phase-1
13	Only One level of DRB approval is considered for estimations.	Phase-1
14	Only one base template for documentation generation is in Scope and we will reuse existing functionality from LC market. Contract rationalization not in scope (LLA teams to rationalize contract).	Phase-1
15	If line item quantity is more than 1, line items will be split during Opportunity to Order conversion.	Phase-1
16	Salesforce will not generate Circuit IDs. Agents will create and update Circuit IDs on Order Line Items.	Phase-1
17	We will use the existing Work Order Automation process. Agents to update the billing/provisioning systems manually while processing Work Orders in Salesforce. (Option A)	Phase-1
18	The existing LATAM custom assetization process will be used to create assets after order completion for Caribbean markets.	Phase-1
19	Once an Opportunity is converted into an Order, it is treated as the “point of no return”.	Phase-1
20	Enhanced Account UI will use the existing Customer C360 view, adjusted to fit the current Account data model. It will include only: ▪ Account details ▪ Related Contacts ▪ Related Billing Accounts available in Salesforce (no integrations) ▪ Locations ▪ Related Salesforce Cases	Phase-1
21	Analytics and reporting are not included in scope.	Phase-1 and 2
22	Salesforce will manage the above sales-flow scenarios internally. Agents will manually perform required actions in external systems (e.g., billing/fulfilment platforms) and update Salesforce accordingly.	Phase-2
23	The “point of no return” will be when an Opportunity is converted to an Order. After Order creation, changes will be handled through the defined order/change processes.	Phase-2

Company Confidential © Capgemini 2026. All rights reserved.

Assumptions

Sr No.	Key Delivery Assumptions	Applicable Phase
24	Phase 2 will support the following MACD (Move, Add, Change, Disconnect) scenarios within Salesforce: **Fixed Lines** - Move (Physical Location change), Disconnect, Change Plan (Upgrade/Downgrade), Port Out, Add/Change Addon, Suspend/Resume Voluntary, Suspend/Resume Nonpay (Dunning Process), Change MSISDN (port or host), Change Device, Contract Renewal **Mobile Lines** - Move (Transfer Account), Disconnect, Change Plan (Upgrade/Downgrade), Port Out, Add/Change Addon, Suspend/Resume Voluntary, Suspend/Resume Nonpay (Dunning Process), Change MSISDN (port or host), Change Device, SIM Swap/Change, Contract Renewal.	Phase-2
25	The Dunning (non-pay suspend/resume) and Voluntary suspend/resume processes will be reused from the existing solution delivered under the Service Manager project.	Phase-2
26	UAT or E2E testing will be performed by business users from LLA.	Phase-1 and 2
27	Formal design decisions documented as part of the solution design development represent an agreement between parties that were part of making that decision. Any change or contradiction to agreed decisions are understood to impact design development and potentially project timelines.	Phase-1 and 2
28	All parties acknowledge that any change or deviation from the original scope and/or delay in provision or completion of an activity required to support the project delivery will have an impact on the delivery team's ability to deliver within the originally defined project timelines. Therefore, requiring potential changes & raising a CR to the update/extend the target delivery dates and cover the delay cost	Phase-1 and 2
29	Performance testing includes only end to end transaction completion time. No load testing or concurrent user testing is in scope	Performance Testing
30	As part of Data Mapping & Transformation field mapping should be signed-off before build starts; any additions/changes post sign-off follow change control.	Phase 2
31	Current APIs in scope to integrate between Salesforce and Billing systems (Liberate and Cerillion) are: POST TMF 629 (Customer), POST TMF 666 (Account), and POST/GET TMF 622 (Product Order). These existing APIs will be leveraged "as is" based on previous Billing Integration program implementation for current "In Scope" Products provisioning. (Option-B) Any additional changes to these APIs or any new API would need to be considered as separate scope for efforts estimation, Design and implementation – Additional Commercials provided for these Integrations on slide 44	Phase-1 and 2

Company Confidential © Capgemini 2026. All rights reserved.

Dependencies

Sr No.	Key Dependencies	Criticality
1	Prior to the start of the project, LLA should provided at least 2 Product Families related rationalized products to start Design phase for Product Configuration.	High
2	LLA to provide remaining 5 Product Families related rationalized products in first 4 weeks of project commencement.	High
3	LLA to confirm user personas in scope before Design phase for Sales process.	High
4	LLA to provide Data volumetrics and sample data for Data Migration design phase as an input.	High
5	LLA will be responsible to ensure Data Quality and Accuracy during Data Migration phase.	High
6	All Technical / Functional Designs should be approved within 3 days of submission to LLA.	High
7	LLA will deliver support from LLA SMEs, 3rd parties and other stakeholders as required to meet the Project Timeline.	Medium
8	LLA to ensure dedicated support capacity or defined SLA based support model from all 3rd Party vendors for duration of this engagement. We see this as a critical dependency as delay on required support from any vendor would have downstream impact on project deliverables.	Medium
9	BAU team to provide walkthrough on Existing E2E Legacy Sales journey and overview on Billing System during the Discovery phase to enable informed design decisions.	Medium
10	Requirement walkthrough, Architecture overview, Low level requirement/Design documents all to be in place for test design.	Medium

Company Confidential © Capgemini 2026. All rights reserved.

Overall Risks

Sr No.	Key Risk	Criticality	Mitigation Plan
1	Any delays by LLA in providing rationalized product details will impact timeline.	High	LLA should provided at least 2 Product Families related rationalized products to start Design phase for Product Configuration. LLA to provide remaining 5 Product Families related rationalized products in first 4 weeks of project commencement.
2	Any delays in confirming User Personas details by LLA would have impact on timelines.	High	LLA should provide User Personas details for at least Phase-1 before commencement of project and remaining personas for Phase-2 can be provided in first 4 week of commencement of the project.
3	Any delays in providing Data volumetrics and sample data for Asset Migration and Account Reconciliation may impact to timeline and efforts.	High	LLA should provide Data migration related details before commencement of Phase-2.
4	Enhancements/Changes to the existing functionality or major design changes are not considered as a part of this proposal.	High	If any will be treated as a Change Request.
5	Any New Product variants to be considered other than In scope Products may have impact on Solutioning & Project Timeline.	High	It may require additional efforts to accommodate new product configuration changes and have direct impact on timelines.
6	Adhoc Devops activities like Refresh of sandboxes, Restructuring of Copado pipelines, reorg of sandboxes and Salesforce upgrades.	High	Adds to overall project efforts and may have impact of timelines.

Company Confidential © Capgemini 2026. All rights reserved.

Out of Scope



- Product Rationalisation
- CLM implementation
- Any Integration from/to Salesforce (Option A only)
  Integration with Amdocs (Option B)
- Any changes to BSS Systems (Liberate, Cerillion and Amdocs)
- Any Changes to Mulesoft
- Testing
  - UAT Testing (CG team will provide support)
  - Security Testing
  - Usability Testing
- Third Party Vendor Management and system availability
- Infrastructure and Network activities
- Consumer support and Clarifications
- Salesforce release management
- SF Platform Licensing

Company Confidential © Capgemini 2026. All rights reserved.

Delivery Plan & Governance Model

Make it real.

Capgemini x LIBERTY LATIN AMERICA

Delivery Plan: Option A (w/o Integration)

Phase 1 - Tasks	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10
Product Design & Configuration										
New Connect – Sales Flow										
• SF										
• UI Enhancements										
• Bulk Upload New Connect										
• Phased UAT										
• Phased Deployments				★			★			

Phase 2- Tasks	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10
MACD – Sales Flow										
• SF										
• Contract Renewal & Dunning										
• Bulk Upload MACD										
• Asset Migration										
• Account Reconciliation										
• Phased UAT										
• Phased Deployments						★				★

Company Confidential © Capgemini 2026. All rights reserved.


Delivery Plan: Option B (Automated Provisioning with As-is existing API's)

Phase 1 - Tasks	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12
Product Design & Configuration												
New Connect – Sales Flow												
• SF + Integration												
• UI Enhancements												
• Bulk Upload New Connect												
• Phased UAT												
• Phased Deployments					★			★				

Phase 2- Tasks	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12
MACD – Sales Flow												
• SF + Integration												
• Contract Renewal & Dunning												
• Bulk Upload MACD												
• Asset Migration												
• Account Reconciliation												
• Phased UAT												
• Phased Deployments									★			★


Company Confidential © Capgemini 2026. All rights reserved.

Governance Structure & Escalation Matrix

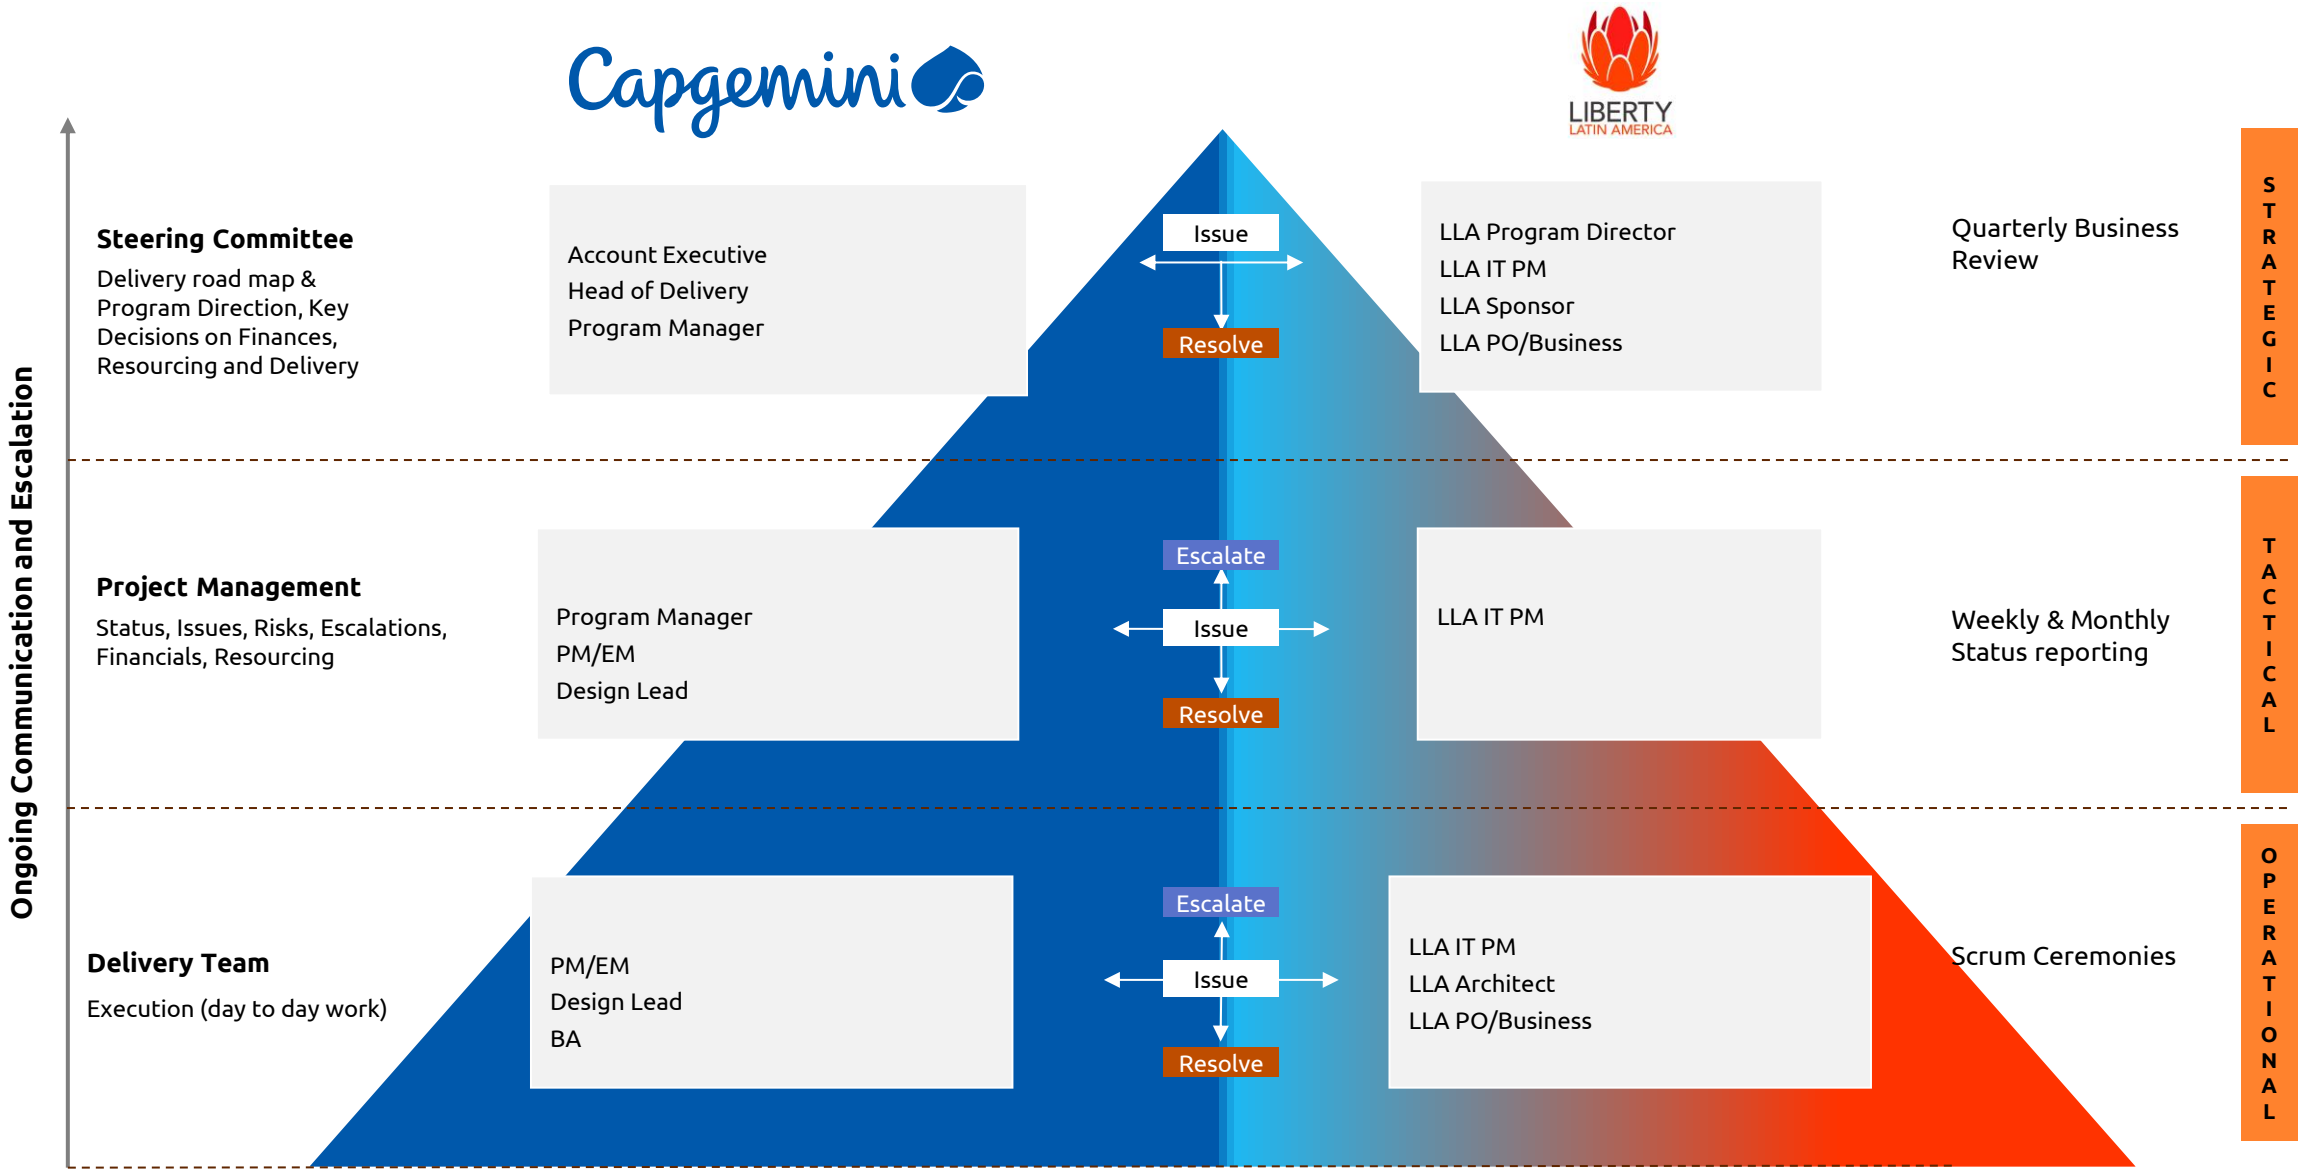

Company Confidential © Capgemini 2026. All rights reserved.

Reporting

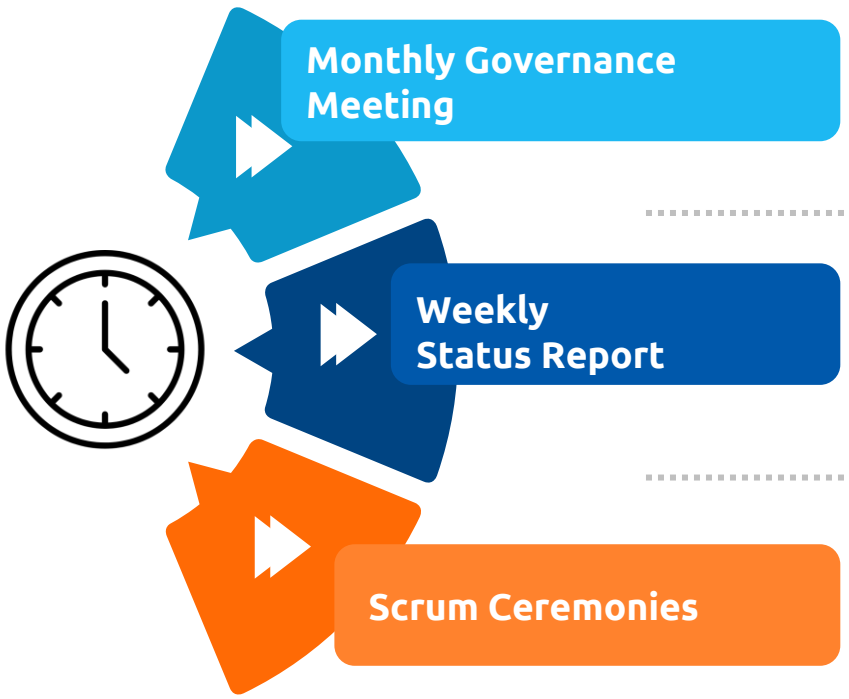

To Include: Program status, Issues, Risks, Program Direction & Manage Capgemini commercial relationship

To Include: Project status, Issues, Risks

To Include: Stand-up meeting, Daily tracking, Task planned, task completed, Retrospection, Show & Tell etc.

Weekly project report will be prepared by the Capgemini EM/PM.

This report will include:

- Summary
- RAG status
- Key change requests and initial impact analysis
- Risks, issues,
- Key dependencies
- Status and project progress

Company Confidential © Capgemini 2026. All rights reserved.

Commercials

Make it real.

Capgemini x LIBERTY LATIN AMERICA

Commercials

CAPGEMINI will deliver scope of work stated in this proposal as a Fixed Price model for **$ 783,718.00 Option A and $1,046,504 for Option B**

The cost breakdown is as follows:

Services	Option A (w/o Integration)	Option B (Automated Provisioning with As-is existing API's)
Phase 1 ▪ Functional Design & Backlog creation ▪ Design, Development & Unit testing ▪ UAT, Pre-prod & PVT Support ▪ QA Testing ▪ UAT Testing Support ▪ Automation & Performance Testing	**$ 491,504.00**	**$ 648,932.00**
Phase 2 ▪ Functional Design & Backlog creation ▪ Design, Development & Unit testing ▪ UAT, Pre-prod & PVT Support ▪ QA Testing ▪ UAT Testing Support ▪ Automation & Performance Testing	**$ 292,214.00**	**$ 397,572.00**
Total Cost	**$ 783,718.00**	**$ 1,046,504.00**

Commercial T&Cs

- The commercials do not include any onsite travel. Any travel & stay at onsite on request of LLA will be charged on actuals.
- The quote is exclusive of any applicable sales tax, service tax, VAT, local taxes & currency exchange rate fluctuations.
- The amount mentioned is subject to local tax. Value added tax may be payable at the applicable local rate, subject to issue by CAPGEMINI of a valid value added tax invoice. In addition, CAPGEMINI alone will bear any taxes related to CAPGEMINI's existence or gross net income taxes based on CAPGEMINI's sales under this CR including any withholding tax with LLA must withhold from payments to CAPGEMINI and to the relevant authority.
- Consequently, CAPGEMINI will not charge LLA or gross up or add on to any fees to LLA for amounts properly withheld by LLA and remitted by LLA to the relevant authority.
- The pricing is for the scope of work and services mentioned in this proposal. Inclusion of any other activity will require rework/re-base lining of the commercials.
- Payment milestones would be monthly, and CAPGEMINI will raise Invoices monthly in arrears
- Hypercare pricing is included as part of each Phase Cost

Company Confidential © Capgemini 2026. All rights reserved.

Full Integration with BSS Systems

- In addition to the two proposed options, we can extend the Automated Provisioning solution (Option B) to include full integration with all three BSS systems, including Amdocs, and also leverage the existing APIs by reusing and enhancing them, along with developing any additional APIs required

- Additional Billing Integration Use Case –
  - Order Provisioning with Liberate, Cerillion and Amdocs
    - Create Customer – TMF629 (Outbound = SF to ESB to Billing)
    - Create Billing Account – TMF666 (Outbound = SF to ESB to Billing)
    - Create Product Order – TMF622 (Outbound = SF to ESB to Billing)
    - Update Order Status – Salesforce REST API (Inbound = Billing to ESB to SF)
  - Above APIs would need to be designed and implemented for New Service and MACD Scenarios.
  - Account Synchronization from Billing to Salesforce (Inbound = Billing to ESB to SF)
  - Asset Synchronization from Billing to Salesforce (Inbound = Billing to ESB to SF)
- Current analysis and estimations show 45% of the current products, product families, and billers are supported via existing ESB integrations. Additional effort noted in this option would be to support all products, families, and billers for the same.

- CAPGEMINI will deliver scope of work stated in this proposal as a suggested Price for ~ $ 1,491,703.00

- Overall duration for this scope will be 15 months


Company Confidential © Capgemini 2026. All rights reserved.

Optional Production Support Model

Make it real.

Capgemini x LIBERTY LATIN AMERICA

Production Support Model



Production Support Model


A robust and well-structured Production Support Model is essential to sustaining the long-term success of the Sales Digital Transformation Rationalization + MACD program. As the solution transitions from deployment to business-as-usual operations, Capgemini's Production Support Model ensures stability, continuity, and proactive management across all Salesforce components.

Our approach is designed to provide seamless operational support, rapid incident resolution, and continuous optimization, ensuring that Liberty Caribbean B2B can maintain high service levels, protect revenue processes, and scale the solution confidently across markets.

Built on proven telecom delivery practices, the model incorporates tiered support, clear SLAs, structured incident and problem management, regular monitoring, and ongoing enhancements. This ensures that the platform remains resilient, compliant, and performance-optimized while enabling Liberty's teams to focus on commercial growth and customer value.

Company Confidential © Capgemini 2026. All rights reserved.

Production Support lifecycle

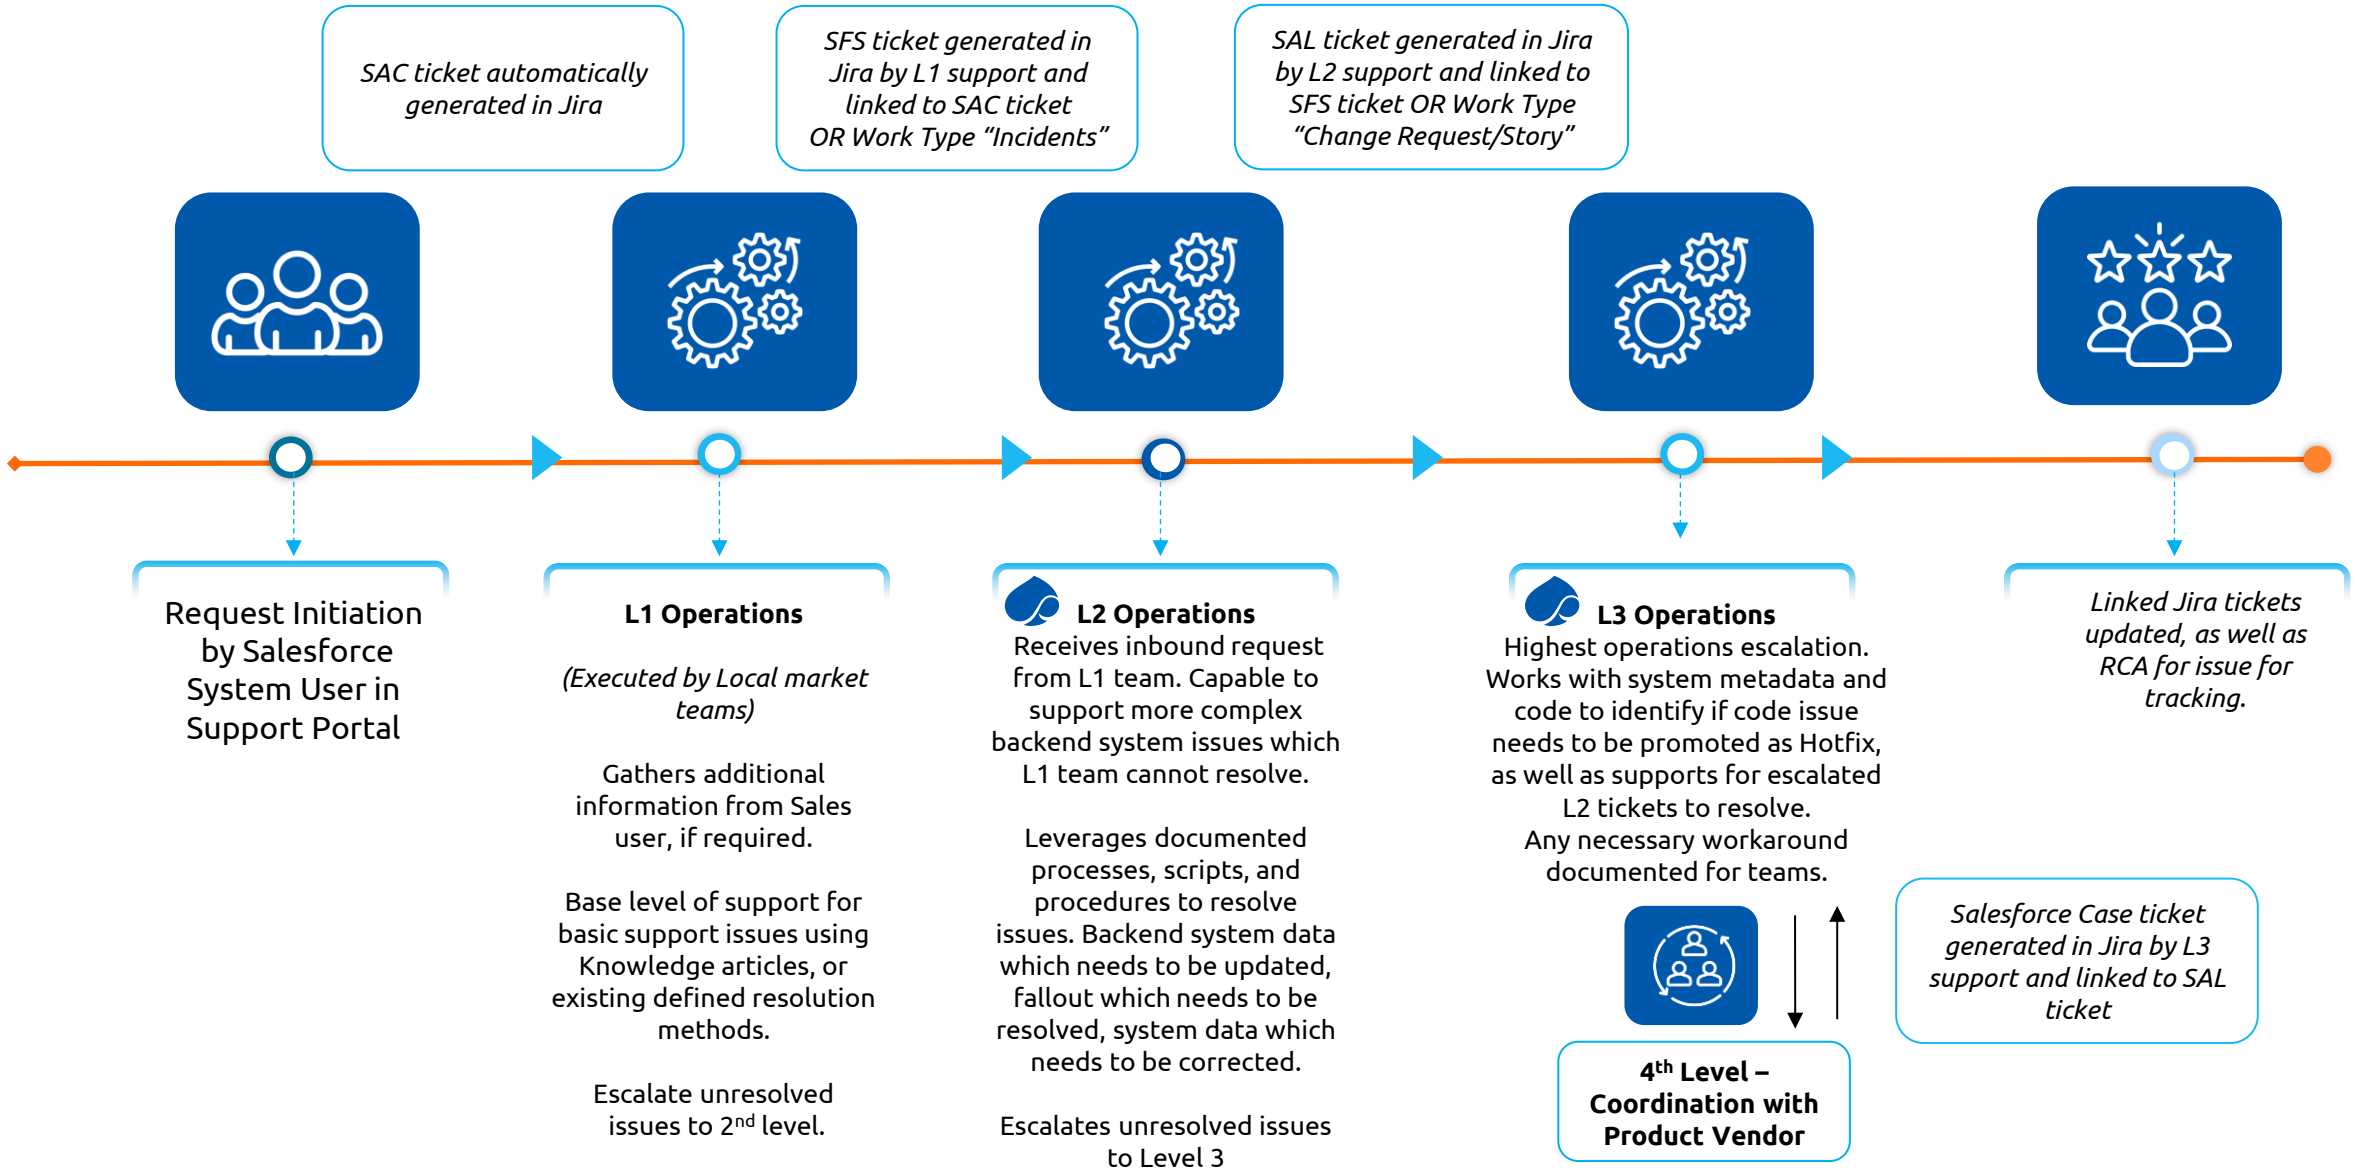

Company Confidential © Capgemini 2026. All rights reserved.

What B2B SF L2 & L3 Team does?

SCOPE

Track and resolve Incidents, Problems, and Service Requests, related to LC B2B Sales Transformation functionalities in scope.

- Service introduction
- KM: Knowledge Management
- Incident Management
- L2/L3: Problem Management
- SR: Service Requests /CR: Change Request
  < 3 PD – Depends on capacity

LLA Operations team will manage
L1: Helpdesk and Triaging &
L2: Service Restoration (Platform related)

PROCESS & FUNCTIONAL MODULES COVERED

Process: The SF L2 & L3 Team will work in conjunction SAFe, DevOps and ITIL framework as a single team.

Technology: SF, Copado, Bitbucket, VS Code Studio, Notepad++, Postman

OpCo: Caribbean

COVERAGE

Business hours: (8am – 8pm) EST business hours Mon-Fri on Non-Public Holidays

Business Days: Monday - Friday excluding offshore public holidays.

On-call Hours: (Expansion) All times outside the business hours, including weekends (Saturday/Sunday) and offshore public holidays are on-call hours. During this period, a support analyst will be available for all issues other than P1 and for P1 issues the required team will be mobilized to work on priority.

SLA'S & KEY KPI'S

SLA's :

- Time to fix P1, P2, P3, P4

Key KPI's:

- % of SLA achievement on P1,P2,P3,P4
- No of tickets in backlog Profile of Ageing tickets P1, P2, P3, P4

Note – SLAs to be baselined

Company Confidential © Capgemini 2026. All rights reserved.

SLA's & KPI's

Priority	Criteria/Definition (Samples/Examples)
P1 (Critical)	• Complete application's loss of service in production • Order Fulfilment impacting 51-100% of the orders • Financial impact > 1million
P2 (High)	• Partial application's loss of service in production • Order Fulfilment impacting 25% to 50% of the orders • Financial impact between 250k to 1million • Degradation of Performance
P3 (Medium)	• Loss of service for customer • Order fulfilment for separate orders • Complete or Partial loss of service on QA
P4 (Low)	• User Access Setup • Price Corrections • Configuration Corrections
P5 / Service Requests	• Not an incident or problem but an enhancement or bulk data fix request • Product Catalogue Management • Configuration Setup/Changes

Priority	Initial Response (Call acknowledged)	Progress Updates	Resolution Time	Target KPI
P1	30 Minutes	Every 1 Hour	4 Business Hours	95%
P2	1 Business Hour	Every 4 Hours	16 Business Hours	95%
P3	1 Working Day	Every 3 Days	24 Business Hours	80%
P4, P5	1 Working Day	N/A (consider as SR)	N/A	-

- There will be a 4 weeks of stabilization period after Phase 1 Production Go-Live
- During the 4 week stabilization period SLA will be measured but not reported
- SLAs will be re-evaluated at the end of stabilization period
- SLAs will be applicable post stabilization period



Company Confidential © Capgemini 2026. All rights reserved.

RoadMap for B2B L2 & L3 Support


1



- **Kick off** with primary scope focusing on L2 & L3 support for SF B2B LC OpCo
- Based on the volumetric analysis Team composition and capacity will be organized

(Kick off)

2



- **Extend the service coverage** window
- Establish and agree E2E support process, R&R and RACI for SF B2B (for L2 & L3)

(Stabilise)

Well-defined SF/SFI B2B L2 & L3 Operating Model

SIAM Governance will be extended for B2B L2 & L3 Support as well

- **KPI/SLA drive** "Service Introduction and management team"
- **Unified SF/SFI services** view from design, development to L2 & L3 (aligned to SAFe, DevOps and ITIL framework)



(Run)

To-Be State
Improved Business KPIs



Key Considerations :

- Team Structure: 1 Offshore & 1 Onshore SF Dev FTE's
- The current L2 & L3 Support team of CARE can also be mutualized in this support model provided there contract is extended

Company Confidential © Capgemini 2026. All rights reserved.

Commercials

The cost breakdown is as follows:

Services

Capgemini shall deliver Level 2 (L2) and Level 3 (L3) Production Support services for a period of one (1) year on a fixed-price basis at a total contract value of **$ 155,818.00**

Commercial T&Cs

- The commercials do not include any onsite travel. Any travel & stay at onsite on request of LLA will be charged on actuals.
- The quote is exclusive of any applicable sales tax, service tax, VAT, local taxes & currency exchange rate fluctuations.
- The amount mentioned is subject to local tax. Value added tax may be payable at the applicable local rate, subject to issue by CAPGEMINI of a valid value added tax invoice. In addition, CAPGEMINI alone will bear any taxes related to CAPGEMINI's existence or gross net income taxes based on CAPGEMINI's sales under this CR including any withholding tax with LLA must withhold from payments to CAPGEMINI and to the relevant authority.
- Consequently, CAPGEMINI will not charge LLA or gross up or add on to any fees to LLA for amounts properly withheld by LLA and remitted by LLA to the relevant authority.
- The pricing is for the scope of work and services mentioned in this proposal. Inclusion of any other activity will require rework/re-base lining of the commercials.
- Payment milestones would be monthly, and CAPGEMINI will raise Invoices monthly in arrears

Company Confidential © Capgemini 2026. All rights reserved.

Future Roadmap

Make it real.

Capgemini x LIBERTY LATIN AMERICA


Future Roadmap

Phase 1 and 2 are part of this Proposal

- MACD Sales Flow for Enterprise Caribbean Market
- Bulk MACD
- Asset Migration & Account Cleanup

- Product Rationalization or introduction of new products
- Extension to any other markets

Capgemini can offer support for Product Rationalization and related capabilities which are detailed in next 2 slides

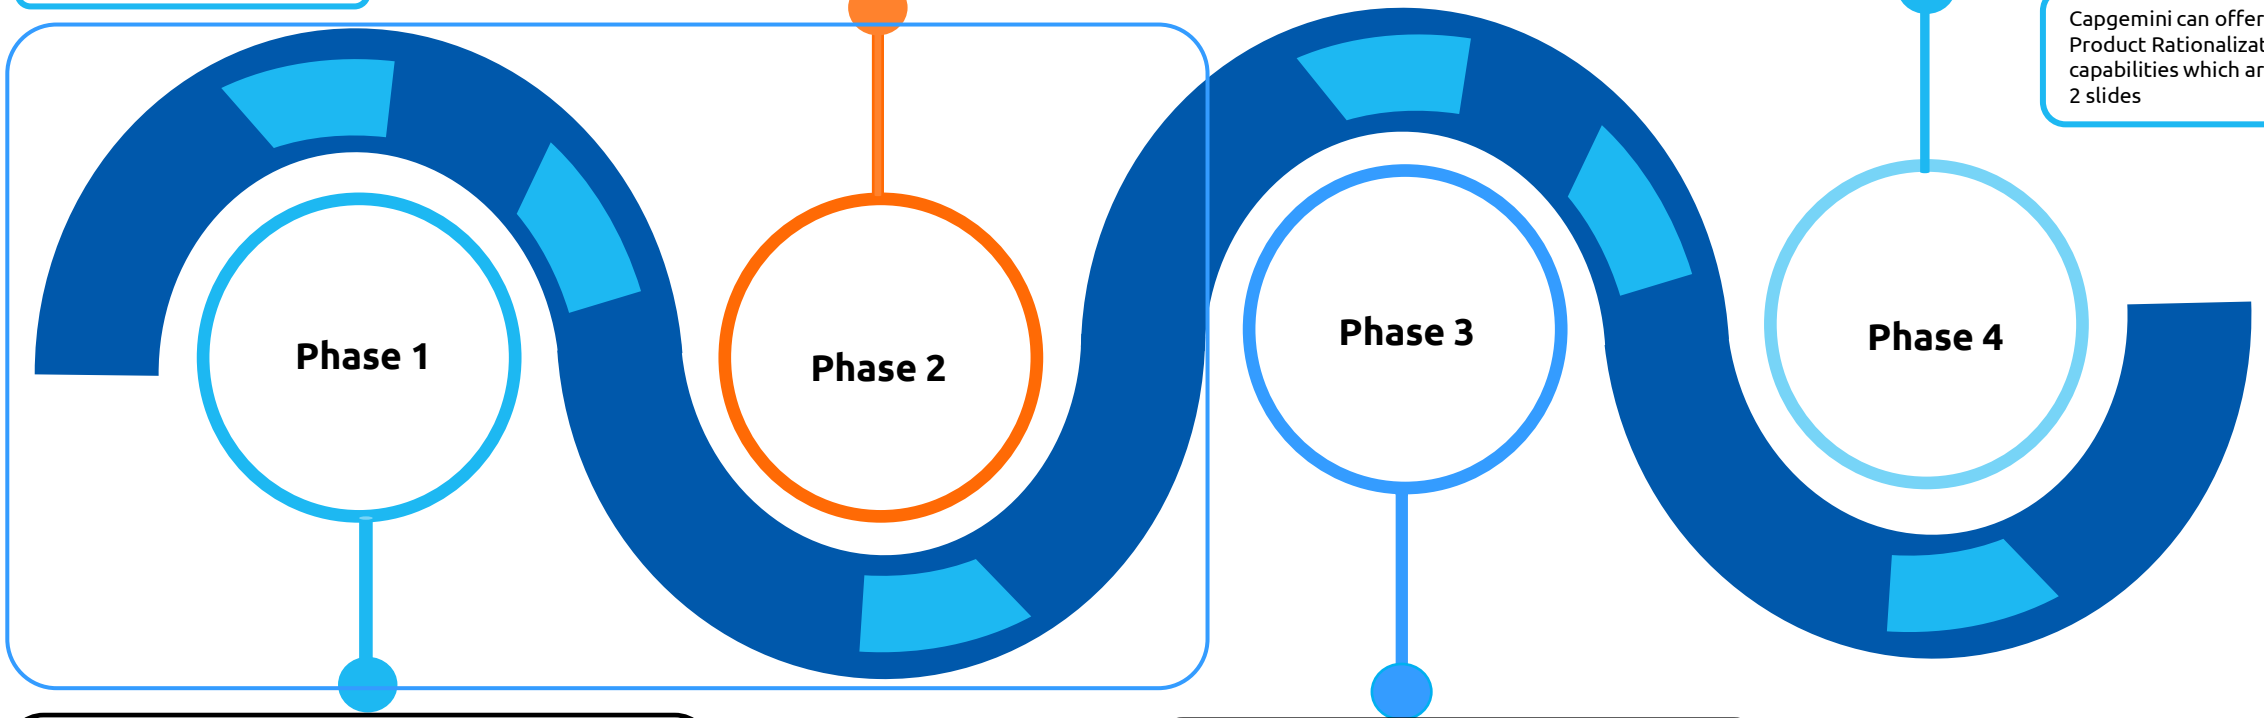

- SF Product Configuration for Priority Caribbean Markets
- Sales Flow for New Connect journey for Enterprise Caribbean Markets.
- Bulk New Connect and UI Enhancements

- Billing Integration for Provisioning and Asset/Account Sync up
- Integration with other systems for Credit Check etc.
- Agentforce Usecases

Company Confidential © Capgemini 2026. All rights reserved.

Our Approach Towards Product Rationalization


Product Portfolio Assessment & Roadmap	Product Modelling & PLM Process Reengineering	Data Flows & KPI Management	Operational Alignment & Benefit Tracking
Analyze & Rationalize	**Design & Define Strategy**	**Configure & Validate**	**Map & Orchestrate to Billing**
• Kick-off workshops: confirm scope, outcomes, timelines, owners, data sources. • Catalog Profiling: inventory SKUs/bundles, hierarchy, metadata, dependencies; remove duplicates/overlaps/promos; segment into 7 families. • Assess performance: revenue, volumes, lines, ARPU/sales, ageing; plus regulatory, contractual, CX, complexity; note country variants. • Decide per product: Retain / Retain-with-changes / Grandfather / Migrate / Retire; log rationale and owners.	• Define end-state product model in Salesforce Legacy Sales Cloud; finalize families/hierarchy and attribute dictionary. • Finalize product family taxonomy and rationalized catalog hierarchy. • Establish attribute dictionary, reuse CSC technical attribute model (as applicable) • Codify lifecycle, naming/SKU/versioning; stop-sell/grandfathering rules; support country variants via rules. • Establish governance (and measurement (Net MRR/NRR, pricing/billing error rate). • Map offers/charges to billing codes; re-engineer processes to future-proof PLM	• Implement DRB/SOF and Sales-Finance-Technical validations • Configure legacy catalog; leverage Vlocity EPC/CPQ framework for technical attributes; set eligibility rules and cardinalities • Define product model data flows (Opportunity → Quote/Order → Assetization) and enforce attribute validation • Establish pricebooks, Enforce promo/discount guardrails • Measure KPIs (MRR/NRR) by tagging MACD, quantify customer/revenue/ cost impact, iterate the benefits-realization plan	• Define MACD semantics, mapping transactions to amend/swap/suspend/ re-rate/recontract, include bulk patterns. • Refine Product–Billing mapping, realign processes/integrations; assetize at order completion, sync to Salesforce. • Apply country/regulatory taxes, surcharges, and treatments in mapping/orchestration. • Execute cutover/change, track SKU reduction, MACD lead time, pricing/billing error rate, and Net MR
Key Outputs			
✓ *Rationalization decision log* ✓ *Prioritized wave plan*	✓ *Target catalog blueprint* ✓ *Attribute dictionary* ✓ *Lifecycle & governance playbook*	✓ *Configured catalog & rules,* ✓ *Validated flows* ✓ *UAT sign-off package*	✓ *Mapping matrix* ✓ *Orchestration updates* ✓ *Cutover plan* ✓ *Benefit dashboards*


Company Confidential © Capgemini 2026. All rights reserved.


Assessment Methodology

Rationalize legacy catalog to a governed, MACD-ready, billing-synchronized model.

- Attribute-driven
- Standardize
- Commercial vs Technical Product Mapping
- Modular
- Country compliant
- Provisioning & billing-aware
- Reuse CSC technical attribute model

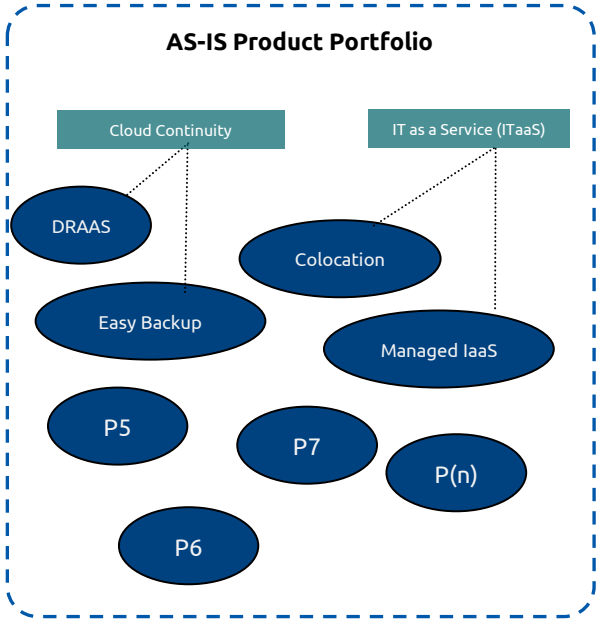

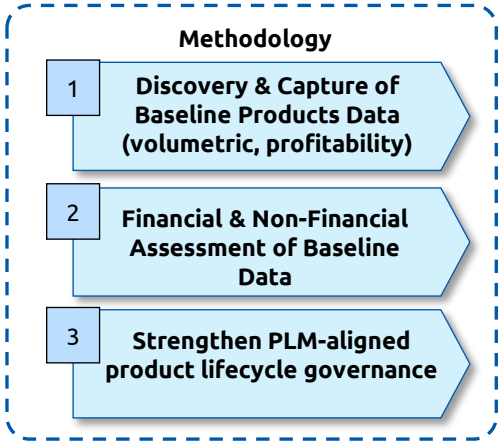

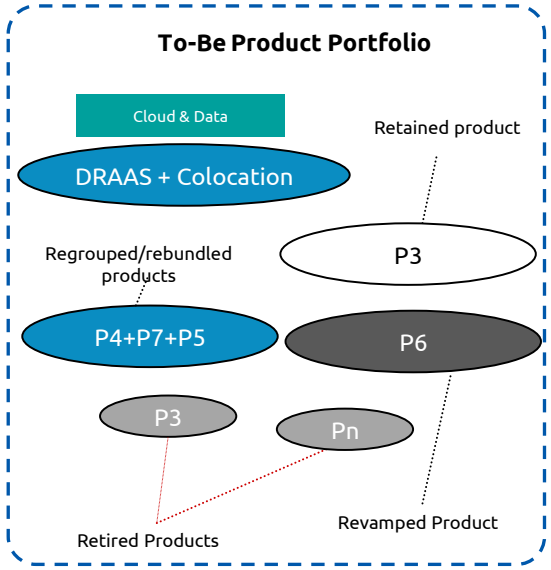

AS-IS Product Family

Product

To-Be Product Family

Company Confidential © Capgemini 2026. All rights reserved.

About Capgemini

Capgemini is an AI-powered global business and technology transformation partner, delivering tangible business value. We imagine the future of organizations and make it real with AI, technology and people. With our strong heritage of nearly 60 years, we are a responsible and diverse group of 420,000 team members in more than 50 countries. We deliver end-to-end services and solutions with our deep industry expertise and strong partner ecosystem, leveraging our capabilities across strategy, technology, design, engineering and business operations. The Group reported 2024 global revenues of €22.1 billion.

Make it real.
www.capgemini.com

DISCLAIMER:

The information contained within this proposal is and shall remain the property of Capgemini UK plc. This proposal is supplied in strict confidence and must not be produced in whole or in part, used in tendering or for manufacturing purposes or given or communicated to any third party without the prior written consent of Capgemini UK plc.

DISCLOSURE OF INFORMATION:

This proposal is supplied in strict confidence and the information contained in this proposal includes information the disclosure of which would be likely to cause significant harm to Capgemini's commercial interests. Therefore, information contained in this proposal must not be disclosed (in whole or in part) in response to a request for information under the Freedom of Information Act 2000 without Capgemini's prior written consent.

© Capgemini 2026



This presentation contains information that may be privileged or confidential and is the property of the Capgemini Group.

Copyright © 2026 Capgemini. All rights reserved.
